Inspect Minnesota & Midwest Soil Testing

P.O. Box 383 Hugo, MN 55038

Brian Humpal

651-492-7550/Brian@midwestsoiltesting.com

MPCA Licensed Advanced Inspector

SUBSURFACE SEWAGE TREATMENT SYSTEM (SSTS) COMPLIANCE REPORT

Inspection Address: 7825 Manning Ave S, Denmark Twp, MN 55033

REPORT SUMMARY

I have performed an "MPCA Compliance Inspection" on this system, have reviewed the history of the system with the owner, Pat Ellis, and have reviewed the original design/permit records on file at Washington County. This older system (installed in 1994) consists of two precast septic tanks and a rock trench drainfield. Ron's Septic Service pumped the septic tanks on March 31, 2016.

Predicated on my inspection of the system, my review of the history of the system with the owner, and my review of the original design/permit records, it is my opinion that this system presently meets MPCA minimum compliance inspection requirements.

Inspect Minnesota and Midwest Soil Testing have been hired to perform a compliance inspection of this SSTS for compliance with local ordinances pursuant to Minn. Stat. § 115.55 (2013). This compliance inspection covers only the criteria required by Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011). A compliance inspection is an indication of the current compliance status of the system and does not guarantee the performance or longevity of this system beyond the date of inspection, as it is impossible to determine the future performance of any system. Inspect Minnesota and Midwest Soil Testing disclaim any use of this compliance inspection beyond determining SSTS compliance pursuant to Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011).

Please contact me should you have any questions.

Brian Humpal



Compliance Inspection Form

Existing Subsurface Sewage Treatment Systems (SSTS)

Doc Type: Compliance and Enforcement

Instructions: Inspection results based on Minnesota Pollution Control Agency (MPCA) requirements and attached forms – additional local requirements may also apply.	For local tracking purposes:
Submit completed form to Local Unit of Government (LUG) and system owner within 15 days	
System Status	
System status on date (mm/dd/yyyy): 3/31/2016	
<u> </u>	npliant – Notice of Noncompliance rade Requirements on page 3)
Reason(s) for noncompliance (check all applicable)	
☐ Impact on Public Health (Compliance Component #1) – Imminent threat to ☐ Other Compliance Conditions (Compliance Component #3) – Imminent thr ☐ Tank Integrity (Compliance Component #2) – Failing to protect groundwate ☐ Other Compliance Conditions (Compliance Component #3) – Failing to protect groundwate ☐ Soil Separation (Compliance Component #4) – Failing to protect groundwate ☐ Operating permit/monitoring plan requirements (Compliance Component #4)	reat to public health and safety Fer otect groundwater ater
Property Information Parcel ID# or Sec/Twp/Range	ge:
· · · · · · · · · · · · · · · · · · ·	or inspection: Property Sale
Property owner: Pat & Terry Ellis Owner's por	ohone:
Owner's representative: Gary Dixon (LaBelle Real Estate) Represer	ntative phone: 651-592-0224
	ry authority phone: 651-430-4052
Brief system description: Two pre-cast septic tanks and a rock trench drainfield.	
Comments or recommendations:	
Certification	
I hereby certify that all the necessary information has been gathered to determine the determination of future system performance has been nor can be made due to unknown possible abuse of the system, inadequate maintenance, or future water usage.	
Inspector name: Brian Humpal Certification	ion number: L5342
	nse number: L2896
Inspector signature: Brian Humpal Pho	ne number:651-492-7550
Necessary or Locally Required Attachments	
	local ordinance
☐ Other information (list): Report Summary, Property Information, Disclaimer, Lic	

1.	Impact on Public Health — Compliance component #1 of 5								
	Compliance criteria:				Ve	Verification method(s):			
		vstem discharge sewage to the bound surface.	☐ Yes	⊠ No		Searched for surface outlet Searched for seeping in yard/backup in home			
		rstem discharge sewage to drain tile surface waters.	☐ Yes	⊠ No		Excessive ponding in soil system/D-boxes Homeowner testimony (See Comments/Explanation) "Black soil" above soil dispersal system			
		rstem cause sewage backup into reling or establishment.	☐ Yes	⊠ No		System requires "emergency" pumping Performed dye test			
		Any "yes" answer above indicates the system is an Imminent Threat to Public Health and Safety.				Unable to verify (See Comments/Explanation) Other methods not listed (See Comments/Explanation)			
		omments/Explanation: one of the above found.							
	140	one of the above found.							
2.	т:	ank Integrity Compliance con	ananant	#2 of 5					
<u> </u>	Tank Integrity – Compliance component #2 of 5 Compliance criteria:			#2 01 5	\/a	wification mathod/o\:			
		•			<u> </u>	erification method(s): Probed tank(s) bottom			
		stem consists of a seepage pit, spool, drywell, or leaching pit.	☐ Yes	⊠ No		Examined construction records			
	Se	repage pits meeting 7080.2550 may be mpliant if allowed in local ordinance.				Examined Tank Integrity Form (Attach)			
	Se	ewage tank(s) leak below their signed operating depth.	☐ Yes	⊠ No		Observed liquid level below operating depth Examined empty (pumped) tanks(s)			
		yes, which sewage tank(s) leaks:			☐ Probed outside tank(s) for "black soil"				
	A	ny "yes" answer above indica stem is Failing to Protect Gr				 ☐ Unable to verify (See Comments/Explanation) ☐ Other methods not listed (See Comments/Explanation) 			
		omments/Explanation:							
		wered underwater camera into tanks -	baffles a	nd tank wa	alls OK.				
_	_								
3.	O	ther Compliance Conditions — Compliance component #3 of 5							
	a.	Maintenance hole covers are damage	d, cracked	d, unsecure	ed, or appear	to structurally unsound. ☐ Yes* ☒ No ☐ Unknown			
	b.	ther issues <i>(electrical hazards, etc.)</i> to immediately and adversely impact public health or safety. ☐ Yes* ☒ No ☐ Unkr System is an imminent threat to public health and safety							
		Explain:							
	C.	 System is non-protective of ground water for other conditions as determined by inspector ☐ Yes* ☐ No *System is failing to protect groundwater 							
		Explain:							

Property address: _ 7825 Manning Ave S, Denmark Twp, MN 55033

Inspector initials/Date: 3/31/2016

www.pca.state.mn.us • 651-296-6300 • 800-657-3864 • 3 of 979Y 651-282-5332 or 800-657-3864 • Available in alternative formats wq-wwists4-31 • 1/24/12 Page 2 of 3

1.	Soil Separation — Compliance compor	nent #4 c	of 5			
	Date of installation: 1994	Unkr	nown	V	erification method(s):	
	Shoreland/Wellhead protection/Food Beverage Lodging?	☐ Yes	⊠ No		oil observation does not expire. P	
	Compliance criteria:				bservations by two independent p nless site conditions have been al	
	For systems built prior to April 1, 1996, and	⊠ Yes	☐ No		equirements differ.	
	not located in Shoreland or Wellhead Protection Area or not serving a food, beverage or lodging establishment:				Conducted soil observation(s) (Two previous verifications (AttaNot applicable (Holding tank(s), n	ch boring logs)
	Drainfield has at least a two-foot vertical separation distance from periodically saturated soil or bedrock.				Unable to verify (See Comments/ Other (See Comments/Explanation	Explanation)
	Non-performance systems built April 1,	☐ Yes	☐ No	С	omments/Explanation:	
	1996, or later or for non-performance systems located in Shoreland or Wellhead Protection Areas or serving a food, beverage, or lodging establishment:			R	eviewed design and permit record	ls.
	Drainfield has a three-foot vertical separation distance from periodically saturated soil or bedrock.*					
	"Experimental", "Other", or "Performance"	☐ Yes	□ No	- Ir	ndicate depths of elevations	
	systems built under pre-2008 Rules; Type IV or V systems built under 2008 Rules (7080. 2350 or 7080.2400 (Advanced Inspector License required)			A. Bottom of distribution media B. Periodically saturated soil/bedrock C. System separation		See Attached Boring Log(s)
	Drainfield meets the designed vertical					
	separation distance from periodically saturated soil or bedrock.					
				D.	Required compliance separation*	
Any "no" answer above indicates the system is Failing to Protect Groundwater. *May be reduced up to 15 percent if allowed by Local Ordinance.					f allowed by Local	
5.	Operating Permit and Nitrogen B	MP* – C	Complianc	e com	ponent #5 of 5 🔀 Not app	licable
	Is the system operated under an Operating Permit?					
	Is the system required to employ a Nitrogen BMP?					
	BMP=Best Management Practice(s) specifi	ied in the	system de	sign		
	If the answer to both questions is "no",	this sec	tion doe	s not r	need to be completed.	
	Compliance criteria					
	a. Operating Permit number: Have the Operating Permit requirements been met?				☐ Yes ☐ No	
b. Is the required nitrogen BMP in place and properly functioning?				Yes No		
	Any "no" answer indicates Noncom	pliance	-			

Inspector initials/Date: 3/30/2016

Upgrade Requirements (Minn. Stat. § 115.55) An imminent threat to public health and safety (ITPHS) must be upgraded, replaced, or its use discontinued within ten months of receipt of this notice or within a shorter period if required by local ordinance. If the system is failing to protect ground water, the system must be upgraded, replaced, or its use discontinued within the time required by local ordinance. If an existing system is not failing as defined in law, and has at least two feet of design soil separation, then the system need not be upgraded, repaired, replaced, or its use discontinued, notwithstanding any local ordinance that is more strict. This provision does not apply to systems in shoreland areas, Wellhead Protection Areas, or those used in connection with food, beverage, and lodging establishments as defined in law.

800-657-3864 • 4 of ISTY 651-282-5332 or 800-657-3864 • Available in alternative formats wq-wwists4-31 • 1/24/12 Page 3 of 3

Property address: 7825 Manning Ave S, Denmark Twp, MN 55033

Inspect Minnesota & Midwest Soil Testing


Subsurface Sewage Treatment System Owner/Property Information

This information will be used for the purpose of conducting an MPCA Compliance Inspection.

Date of Inspection: March 31, 2016	Time: 12:00 PM				
Property Address: 7825 Manning Ave S, Denmark	Twp, MN Zip: 55033				
Property Owner: Pat & Terry Ellis	Phone:				
Tank(s) Tank(s)Material Soil Tre Septic 2 □ Fiberglass □ Rock □ Aerobic □ Plastic □ Grave □ Lift □ Metal □ Chan	atment System trench Alternative system Experimental system Description Descri				
	·				
Year house built: 1880 Year septic installed:					
	Number of residents in home? 2-5				
	s drained by gravity? Y				
\mathcal{E} 1	hirlpool bath? N				
More than one system (laundry, etc.)? N					
Does this property have any footing drain tiles conn	ected to the septic system? N				
Are any buildings on this property such as garages or out-buildings connected to this system? N					
Are there any additional systems on this property se	TVING Other buildings? IN				
Location of septic system on lot? North Side					
Location of water well on lot? West Side	Is the well a deep well? Y				
Have you ever experienced any problems with the system such as: tree roots, sewage back-ups, surfacing of sewage onto the ground, septic tank overflowing, etc.; or have any repairs been made to the system? N If yes, explain:					
When was the system last pumped? 3/31/2016	Name of pumper: Ron's Sewer Service				
How often pumped in previous years? Every 2					
Have you received notices from any government agency concerning this system? N					
Is your property located in a shoreland management area? N					
Do you have any additional information that should be given to the new owner? N					

I hereby certify that the above information is correct to the best of my knowledge. I also understand that if the system is considered "non-compliant/failing" per MPCA rules, that the inspector must by law submit a copy of this report to the local government unit within 15 days of the date of inspection completion. I also agree that unless otherwise noted in this report, that I/we are ultimately responsible for payment of all fees for all work performed relative to this inspection by Inspect Minnesota and Midwest Soil Testing.

Owner/Occupant: Pat Ellis' Signature On File Date: 3/30/2016

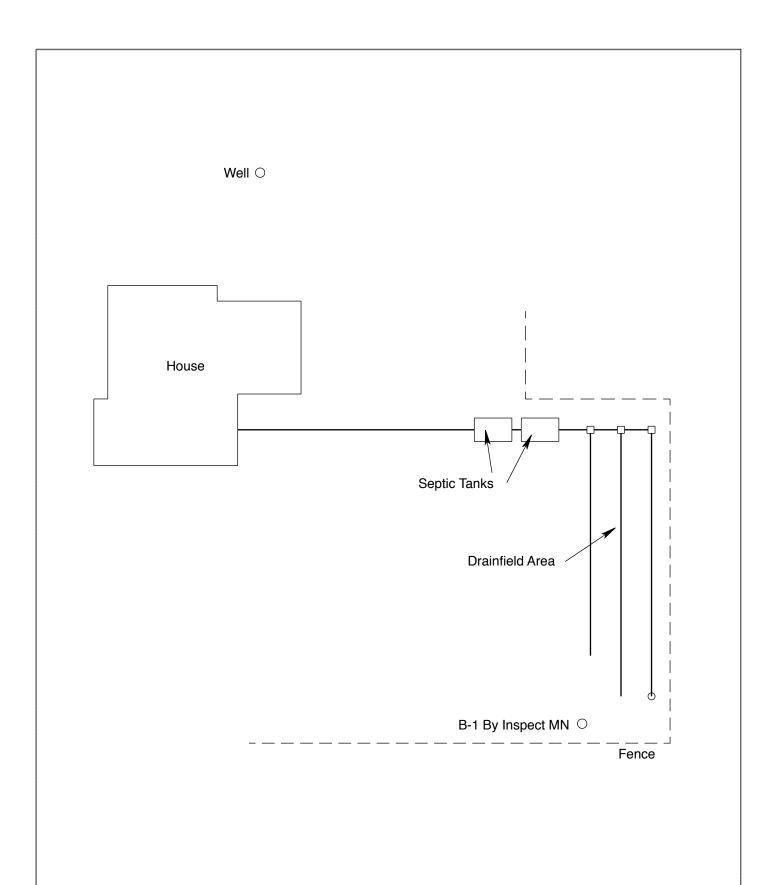

Log Of Soil Borings

Location of Project: 7825 Manning Ave S, Denmark Twp, MN 55033						
Borings Made By: Inspect Minnesota			Date:	3/30/16		
Auger Used: Hand/Bucket		Class	ification System:	USDA		
	Boring Number:	1	Boring Number:			
Surface	L Camo arol	ınd surface as last	Surface			
Elevation	MEI -	nfield trench	Elevation	of		
Boring	uran		Boring			
Depth In	Soils E	ncountered	Depth In	Soils En	Soils Encountered	
Inches 0-12	10VD 2	/2 Silt Loam	Inches			
0-12 12-25		/2 Silt Loam /3 Silt Loam				
25-40		4 Sandy Loam				
40-60		ly Loam With Gravel				
		Rock Fragments sal At 60"				
	Keiu	Sai At 00				
60" Depth To End Of Boring Or Redox			Depth To End Of Bo	oring Or Redox		
Same	The state of the s			•	Relative To System	
-32" Depth To Bottom Of Distribution Media				of Distribution Media		
≥28" Of Separation			Of Separation	DISCIDUCION MEGIC		
End Of Boring At: 60"			End Of Boring At:			
Redox Present At: None			Redox Present At:			
Standing Water Present At: None			Standing	Water Present At:		

Bottom Of Distribution Medium At:	32 Inches


DISCLAIMER

Brian L. Humpal, Inc. dba. Inspect Minnesota, Midwest Soil Testing Relative to Subsurface Sewage Treatment System (SSTS) Compliance Inspections

- 1. This inspection/report is being performed for only the seller/owner of the property on which the SSTS is located. In such case that another party is paying for the inspection, the contract is between only said party and Brian L. Humpal, Inc.; there is no contract between Brian L. Humpal, Inc. and any other party unless otherwise noted.
- 3. Brian L. Humpal, Inc. has not been retained to warranty, guarantee, or certify the proper functioning of the SSTS for any period of time beyond the date of inspection or into the future. Because of the numerous factors (usage, maintenance, soil characteristics, previous failures, etc.) which may affect the proper operation of an SSTS, as well as the inability of Brian L. Humpal, Inc. to supervise or monitor the use or maintenance of the SSTS, the report shall not be construed as a warranty by Brian L. Humpal, Inc. that the SSTS will function properly for any particular party for any period of time.
- 4. Brian L. Humpal, Inc. is unable to verify the frequency and/or, quality of prior or future maintenance of the SSTS. Maintenance of the tank(s) must be performed through the tanks maintenance hole. The removal of solids from any location other than the maintenance hole is not a compliant method of maintenance. It is strongly recommended that maintenance covers be made accessible to the ground surface to facilitate proper maintenance.
- 5. Minimum Compliance Inspection requirements relative to this inspection and this report include <u>only</u> verification that the SSTS has tank(s) (septic tanks, lift tanks, dosing tanks, stilling tanks, etc.) which are watertight below the designed operating depth, the required separation between the bottom of the subsurface soil distribution medium and seasonally saturated soils, no back-ups of sewage into the dwelling, no discharge of sewage/effluent to the ground surface or surface waters, and no imminent safety hazards. Brian L. Humpal, Inc. does not inspect plumbing or pumps prior to the first SSTS component as these are plumbing components. The performance of exterior pumps and associated components are not inspected as they are considered to be maintenance items. Additionally, no indications relative to compliance with electrical code requirements have been made. It is recommended that any other applicable plumbing, electrical, housing, etc. inspections be performed by a qualified inspection business. Sewage back-up verification is limited to observing the floor drain area and/or the information supplied by the last occupants of the building prior to inspection. Brian L. Humpal, Inc. cannot guarantee that the information given to them by the last occupants of the building prior to inspection relative to back-ups is accurate.
- 4. Certification of this SSTS does not warranty future use beyond the date of the inspection. Any SSTS, old or new, can become hydraulically overloaded or discharge sewage/effluent to the ground surface as a result of more people moving into the house than were previously occupying the house, improper maintenance, heavy usage, leaking plumbing fixtures, groundwater infiltration, tree roots, freezing conditions, surface drainage problems, poor initial design, poor construction practices, or unsuitable materials used in constructing the system; the system can also simply stop working because of its age. An SSTS that has been properly designed and installed, properly maintained, and used in the manner for which the system was designed can be expected to provide service for twenty to twenty-five years on average. Some parts of the SSTS such as alarms, switches, pumps, filters, etc. will most likely have to be repaired or replaced over the lifetime of the system.
- 5. A Compliance Inspection is not meant to be a test or inspection for longevity of the system; a Compliance Inspection is strictly for the purpose of determining if the SSTS is protective of public health and safety, as well as the groundwater at the date and time the inspection was performed. This inspection is not intended to determine if the SSTS was originally designed or installed to past or present MPCA or other Local Government Unit code requirements. This inspection is not intended to determine if the SSTS was designed and/or installed to support the anticipated flow from the building as the use of the building may have changed since the design and construction of the SSTS due to the addition of bedrooms, occupants, etc. In addition, this inspection is not intended to determine the quality of the original SSTS design, the quality of the construction practices used while installing the SSTS, or the quality of the materials used in constructing the SSTS.
- 6. Brian L. Humpal, Inc. cannot guarantee the performance of SSTS products/components such as: gravelless pipe, chamber trenches, effluent filters, tanks, sewage pre-treatment components, piping, etc. Products such as gravelless pipe are no longer approved for installation in the State of Minnesota and may have a significantly reduced performance and/or life expectancy.
- 7. WINTER WORK: By accepting this report, it is understood that inspections conducted during winter months (approximately November 1st through April 1st) are more difficult to perform because of possible snow cover and/or ground frost. SSTS components such as tanks, maintenance covers, tank inspection pipes, subsurface distribution medium inspection pipes, and soil treatment areas are more difficult or impossible to locate due to snow cover and/or ground frost. In addition, soil borings are more difficult to perform due to snow cover and/or ground frost. Brian L. Humpal, Inc. will attempt to use the same level of standards when performing work during winter periods as when performing work during non-winter periods. However, the recipient of this report understands that because of the aforementioned considerations, the same level of standards may not be possible.
- 8. By accepting this report, the client understands that Brian L. Humpal, Inc. will not be responsible for any monetary damages exceeding the fee for the services provided.

Subsurface Sewage Treatment Systems

Non-transferable



License # L2896

Date of Issuance:

Maintainer License Expires:
Installer License Expires:
Adv Inspector License Expires:
Dec 22, 2016

Inspect Minnesota, Midwest Soil Testing

Designated Certified Individual (DCI)	Certification Type	Certification Expires
Brian L. Humpal	Maintainer (Certified)	10/15/2017
Brian L. Humpal	Advanced Designer (Certified)	10/15/2017
Brian L. Humpal	Advanced Inspector (Certified)	10/15/2017
Brian L. Humpal	Installer (Certified)	10/15/2017
Brian L. Humpal	Service Provider (Certified)	10/15/2017
Christopher R. Uebe	Designer (Certified)	03/04/2018
Christopher R. Uebe	Inspector (Certified)	03/04/2018



St. Paul, Minnesota 55155-4194

Steven Giddings Manager Environmental Business Assistance Section
