# **Midwest Sewer Services**

| P.O. Box 10853 White I  | Bear Lake, MN 55110   | Brian Humpal                     |  |  |
|---|-----------------------|----------------------------------|--|--|
| 651-492-7550/Brian@M  | idwestsoiltesting.com | MPCA Licensed Advanced Inspector |  |  |
| SUBSURFACE SEWAGE TREATMENT SYSTEM (SSTS) COMPLIANCE REPORT         |                       |                                  |  |  |
| Date: July 30, 2020   | <b>Time:</b> 9:15 AM  | Owner: Rick Verner               |  |  |
| Inspection Address: 12685 170 <sup>th</sup> St N, May Twp, MN 55047 |                       |                                  |  |  |

# **REPORT SUMMARY**

I have performed an "MPCA Compliance Inspection" on this system, have reviewed the history of the system with the owner, Rick Verner, and have reviewed the original design/permit records on file at Washington County. This very old system (installed in 1973) consists of a precast septic tank and a rock trench drainfield. It should be noted that the average life expectancy of a septic system is approximately 30 years.

My inspection indicates that this system is presently "non-compliant" in accordance with MPCA rules 7080.1500 Subp.4(B)(D) because of the lack of the required three foot separation between the bottom of the drainfield and seasonally saturated soils.

In accordance with MPCA rules, I am sending a copy of this complete report to Washington County. I cannot officially speak on behalf of the County relative to the upgrade requirements of these non-compliant systems. Please contact the Washington County Department of Public Health & Environment (651-430-6655) to verify the County's position.

Please advise buyer, agents, lender, etc. to contact me should they have any questions regarding this system.

Christopher Uebe

Brian Humpal

Brian Humpal

| Minnesota Pollution |
|---------------------|
| Control Agency      |

520 Lafayette Road North St. Paul, MN 55155-4194

# **Compliance Inspection Form**

# Existing Subsurface Sewage Treatment Systems

(SSTS)

Doc Type: Compliance and Enforcement

| Instructions: Inspection results based on Minnesota Pollut  | ion Control Agency (MPCA) |
|---|---------------------------|
| requirements and attached forms – additional local requirem | ents may also apply.      |

For local tracking purposes:

Submit completed form to Local Unit of Government (LUG) and system owner within 15 days

## System Status

System status on date (mm/dd/yyyy): 7/30/2020

### Compliant – Certificate of Compliance

(Valid for 3 years from report date, unless shorter time frame outlined in Local Ordinance.)

# Noncompliant – Notice of Noncompliance

(See Upgrade Requirements on page 3)

#### Reason(s) for noncompliance (check all applicable)

- Impact on Public Health (Compliance Component #1) Imminent threat to public health and safety
- Other Compliance Conditions (Compliance Component #3) Imminent threat to public health and safety
- Tank Integrity (Compliance Component #2) Failing to protect groundwater
- Other Compliance Conditions (Compliance Component #3) Failing to protect groundwater
- Soil Separation (Compliance Component #4) Failing to protect groundwater
- Operating permit/monitoring plan requirements (Compliance Component #5) Noncompliant

## **Property Information**

Parcel ID# or Sec/Twp/Range:

| Property address:                             | 12685 170 <sup>th</sup> St N, May Twp, MN 55047    | Reason for inspection: Property Transfer  |
|---|--|---|
| Property owner:                               | Rick Verner  | Owner's phone: 651-353-5283               |
| or  |  |   |
| Owner's representa                            | tive:  | Representative phone:                     |
| Local regulatory authority: Washington County |  | Regulatory authority phone: _651-430-6655 |
| Brief system descrip                          | otion: A pre-cast septic tank and a rock trench of | drainfield.                               |
|   | mondational  |   |

Comments or recommendations:

# Certification

I hereby certify that all the necessary information has been gathered to determine the compliance status of this system. No determination of future system performance has been nor can be made due to unknown conditions during system construction, possible abuse of the system, inadequate maintenance, or future water usage.

| Inspector name:     | Brian Humpal/Christopher Uebe | Certification number:     | C5342/C9852  |
|---------------------|-------------------------------|---------------------------|--------------|
| Business name:      | Midwest Sewer Services        | License number:           | L2896        |
| Inspector signature | e: Brian Humpal After the     | Phone number:             | 651-492-7550 |
| Necessary or        | Locally Required Attachments  |                           |              |
| 🛛 Soil boring lo    | gs                            | 🗌 Forms per local ordinan | се           |
| I Other information | ation (list):                 | Disclaimer, License       |              |
|                     |                               |                           |              |

2 of 9

# 1. Impact on Public Health – Compliance component #1 of 5

Property address: 12685 170th St N, May Twp, MN 55047

#### Compliance criteria: Verification method(s): Searched for surface outlet System discharge sewage to the □ Yes ⊠ No Searched for seeping in yard/backup in home ground surface. Excessive ponding in soil system/D-boxes □ Yes ⊠ No System discharge sewage to drain tile Homeowner testimony (See Comments/Explanation) or surface waters. "Black soil" above soil dispersal system 🗌 Yes 🖾 No System cause sewage backup into System requires "emergency" pumping dwelling or establishment. Performed dye test Any "yes" answer above indicates the system is Unable to verify (See Comments/Explanation) an Imminent Threat to Public Health and Safety. Other methods not listed (See Comments/Explanation) Comments/Explanation:

#### 2. Tank Integrity - Compliance component #2 of 5

| Compliance criteria:  |  | Verification method(s):  |
|---|--|--|
| System consists of a seepage pit, cesspool, drywell, or leaching pit.             | 🗌 Yes 🛛 No   | <ul><li>Probed tank(s) bottom</li><li>Examined construction</li></ul>      |
| Seepage pits meeting 7080.2550 may be<br>compliant if allowed in local ordinance. |  | Examined Tank Integrit   |
| Sewage tank(s) leak below their designed operating depth.                         | 🗌 Yes 🖾 No   | <ul> <li>Observed liquid level be</li> <li>Examined empty (pump</li> </ul> |
| If yes, which sewage tank(s) leaks:   |  | Probed outside tank(s)   |
| Any "yes" answer above indic<br>system is Failing to Protect G                    | ☐ Unable to verify (See Comparing Comparin |  |

Comments/Explanation:

None of the above found.

Lowered underwater camera into tank - baffles and tank walls OK.

Probed tank(s) bottom
Examined construction records
Examined Tank Integrity Form (Attach)
Observed liquid level below operating depth
Examined empty (pumped) tanks(s)
Probed outside tank(s) for "black soil"
Unable to verify (See Comments/Explanation)
Other methods not listed (See Comments/Explanation)

#### 3. Other Compliance Conditions - Compliance component #3 of 5

| a. | Maintenance hole covers are d | lamaged, cracked, u | unsecured, or appear t | o structurally unsound. | Yes* | 🛛 No | Unknown |
|----|-------------------------------|---------------------|------------------------|-------------------------|------|------|---------|

b. Other issues (*electrical hazards, etc.*) to immediately and adversely impact public health or safety.  $\Box$  Yes\*  $\boxtimes$  No  $\Box$  Unknown \*System is an imminent threat to public health and safety

Explain:

c. System is non-protective of ground water for other conditions as determined by inspector Yes\* No \*System is failing to protect groundwater

Explain:

# \_\_\_\_\_ Inspector initials/Date: \_\_\_\_\_7/30/2020

#### **4. Soil Separation** – Compliance component #4 of 5

| Date of installation: 1973  | Unknown      | Verification method(s):   |  |  |  |
|---|--------------|---|--|--|--|
| Shoreland/Wellhead protection/Food Beverage<br>Lodging?   | 🖾 Yes 🗌 No   | Soil observation does not expire. Pr  |  |  |  |
| Compliance criteria:  |              | observations by two independent pa<br>unless site conditions have been alt  |  |  |  |
| For systems built prior to April 1, 1996, and<br>not located in Shoreland or Wellhead<br>Protection Area or not serving a food,<br>beverage or lodging establishment:<br>Drainfield has at least a two-foot vertical<br>separation distance from periodically<br>saturated soil or bedrock. | ☐ Yes ☐ No   | <ul> <li>requirements differ.</li> <li>Conducted soil observation(s) (A</li> <li>Two previous verifications (Attac</li> <li>Not applicable (Holding tank(s), not</li> <li>Unable to verify (See Comments/Explanation</li> <li>Other (See Comments/Explanation)</li> </ul> | ch boring logs)<br>o drainfield)<br>Explanation) |  |  |
| Non-performance systems built April 1,<br>1996, or later or for non-performance<br>systems located in Shoreland or Wellhead<br>Protection Areas or serving a food,<br>beverage, or lodging establishment:   | 🗌 Yes 🖾 No   | Comments/Explanation:   |  |  |  |
| Drainfield has a three-foot vertical separation distance from periodically saturated soil or bedrock.*  |              |   |  |  |  |
| "Experimental", "Other", or "Performance"   | 🗌 Yes 🔲 No   | Indicate depths of elevations   |  |  |  |
| systems built under pre-2008 Rules; Type IV<br>or V systems built under 2008 Rules (7080.<br>2350 or 7080.2400 (Advanced Inspector<br>License required)   |              | A. Bottom of distribution media   | See Attached<br>Boring Log(s)                    |  |  |
| Drainfield meets the designed vertical  |              | B. Periodically saturated soil/bedrock  |  |  |  |
| separation distance from periodically<br>saturated soil or bedrock.   |              | C. System separation  |  |  |  |
|   |              | D. Required compliance separation*  |  |  |  |
| Any "no" answer above indicates t<br>Failing to Protect Groundwater.  | he system is | *May be reduced up to 15 percent if allowed by Local Ordinance.   |  |  |  |
| <b>Operating Permit and Nitrogen BMP*</b> – Compliance component #5 of 5 <b>Not applicable</b>  |              |   |  |  |  |
| Is the system operated under an Operating Permit? Yes Ves No If "yes", A below is required  |              |   |  |  |  |
| Is the system required to employ a Nitrogen BMP?  |              |   |  |  |  |
| BMP=Best Management Practice(s) specified in the system design  |              |   |  |  |  |

If the answer to both questions is "no", this section does not need to be completed.

#### **Compliance criteria**

5.

| a. | Operating Permit number:<br>Have the Operating Permit requirements been met? | Yes No |
|----|--|--------|
| b. | Is the required nitrogen BMP in place and properly functioning?              | Yes No |

#### Any "no" answer indicates Noncompliance.


**Upgrade Requirements** (Minn. Stat. § 115.55) An imminent threat to public health and safety (ITPHS) must be upgraded, replaced, or its use discontinued within ten months of receipt of this notice or within a shorter period if required by local ordinance. If the system is failing to protect ground water, the system must be upgraded, replaced, or its use discontinued within the time required by local ordinance. If an existing system is not failing as defined in law, and has at least two feet of design soil separation, then the system need not be upgraded, replaced, or its use discontinued, notwithstanding any local ordinance that is more strict. This provision does not apply to systems in shoreland areas, Wellhead Protection Areas, or those used in connection with food, beverage, and lodging establishments as defined in law.

# <u>Midwest Sewer Testing</u> Subsurface Sewage Treatment System Owner/Property Information

| This information will be used for the purpose of conducting an MPCA                               |                                 |  |  |  |
|---|---------------------------------|--|--|--|
| Date of Inspection: July 30, 2020   | Time: 9:15 AM                   |  |  |  |
|   |                                 |  |  |  |
| Property Address: 12685 170 <sup>th</sup> St N, May Twp, MN                                       | Zip: 55047                      |  |  |  |
| Property Owner: Rick Verner   | Phone: 651-353-5283             |  |  |  |
| Tank(s)         Tank(s)Material         Soil Treatment System                                     | Other                           |  |  |  |
| Septic 1 Fiberglass Rock trench   | Alternative system              |  |  |  |
| Aerobic  Plastic  Gravelless trench    Lift  Metal  Chamber trench                                | Experimental system             |  |  |  |
| Holding Concrete Seepage bed  | Cesspool system<br>Other system |  |  |  |
| Other: Block Mound  |                                 |  |  |  |
| Other At-grade  |                                 |  |  |  |
| Are the tank maintenance covers accessible? $\boxtimes$ Yes $\square$ No *If                      | no, proper maintenance must be  |  |  |  |
| performed through the maintenance holes. Maintenance hole cover                                   |                                 |  |  |  |
| the ground surface to facilitate access and proper maintenance of t                               |                                 |  |  |  |
|   |                                 |  |  |  |
|   | Tank size (gals.): 1200         |  |  |  |
|   | sidents in home? 1-4            |  |  |  |
| Number of bedrooms? 4Are all floors drained by group  |                                 |  |  |  |
| Garbage disposal? Y Whirlpool bath?   | N                               |  |  |  |
| More than one system (laundry, etc.)? N   |                                 |  |  |  |
| Does this property have any footing drain tiles connected to the se                               | ptic system? N                  |  |  |  |
|   |                                 |  |  |  |
| Are any buildings on this property such as garages or out-buildings connected to this system? N   |                                 |  |  |  |
|   |                                 |  |  |  |
|   |                                 |  |  |  |
| Are there any additional systems on this property serving other bu                                | ildings? N                      |  |  |  |
|   |                                 |  |  |  |
| Location of septic system on lot? West Side   |                                 |  |  |  |
| Location of water well on lot? North Side Is the  | e well a deep well? Y           |  |  |  |
| Have you ever experienced any problems with the system such as                                    | tree roots, sewage back-ups,    |  |  |  |
| surfacing of sewage onto the ground, septic tank overflowing, etc.; or have any repairs been made |                                 |  |  |  |
| to the system? N If yes, explain:   |                                 |  |  |  |
|   |                                 |  |  |  |
|   |                                 |  |  |  |
| When was the system last pumped? 2017 Name of pum   | per: Smilie's Sewer Service     |  |  |  |
|   | on a monitoring plan? N         |  |  |  |
| Have you received notices from any government agency concerning this system? N                    |                                 |  |  |  |
| Is your property located in a shoreland management area? Y  |                                 |  |  |  |
| Do you have any additional information that should be given to th                                 | e new owner? N                  |  |  |  |
|   |                                 |  |  |  |

I hereby certify that the above information is correct to the best of my knowledge. I also understand that if the system is considered "non-compliant/failing" per MPCA rules, that the inspector must by law submit a copy of this report to the local government unit within 15 days of the date of inspection completion. I also agree that unless otherwise noted in this report, that I/we are ultimately responsible for payment of all fees for all work performed relative to this inspection by Inspect Minnesota and Midwest Soil Testing

Owner/Occupant:

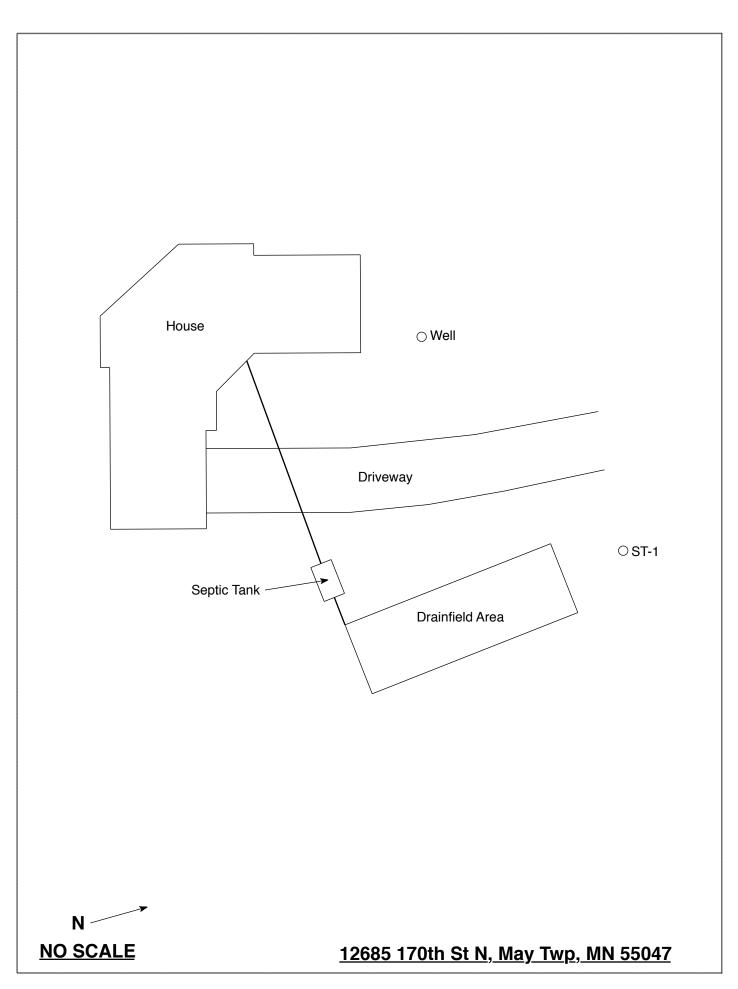

# Soil Observations Log

|  | Location of Project: 12685 170th St N, May Twp, MN 55082 |  |   |                    |                           |                |                         |
|--|--|--|---|--------------------|---------------------------|----------------|-------------------------|
| Observations Made By: Midwest Sewer Se |  |  |   |                    | Date:                     | 7/30/2020      |                         |
| C                                      | lassific   | ation System:  | USDA  |                    |                           |                |                         |
|  | Soil   | Observation:   | ST-1  |                    | Soil C                    | bservation:    |                         |
| Surf<br>Elevat<br>Observ               | ion of   | -  | nd surface as last<br>field trench  | Elevat             | face<br>tion of<br>vation |                |                         |
| Depth In<br>Inches                     | Rock %   | <u>Soils E</u>   | ncountered  | Depth In<br>Inches | Rock %                    | <u>Soils</u>   | Encountered             |
| 0-13<br>13-33<br>33-42<br>42-51        |  | 10YR 4/3 M<br>Fine S<br>10YR 5/2 Medium<br>(Satu<br>Fine S<br>10YR 5/1 Silt Lo | 2 Loamy Sand<br>edium Sand With<br>Sand Layers<br>n Sand(Depleted Matrix)<br>rated) With<br>andy Layers<br>Dam (Depleted Matrix)<br>) With Faint Reds |                    |                           |                |                         |
| 33"                                    | Depth T  | o End Of Soil O  | bservation Or Redox   |                    | Depth T                   | o End Of Soil  | Observation Or Redox    |
| Same                                   |  |  |   |                    | Elevatio                  | on Of Observat | tion Relative To System |
| -48"                                   | Depth T  | o Bottom Of Dis  | stribution Media  |                    | Depth T                   | o Bottom Of I  | Distribution Media      |
|  | Of Sepa  |  |   |                    | Of Sepa                   |                |                         |
| <u> </u>                               |  |  |   |                    |                           | 1              |                         |
| End                                    |  | Observation At:  | 51"   | End Of             |                           | servation At:  |                         |
|  |  | dox Present At:  | 33"   | Chandl             |                           | x Present At:  |                         |
| Stan                                   | Standing Water Present At: 47" At 15 Minutes             |  |   | Standi             | ng Wate                   | r Present At:  |                         |

Bottom Of Distribution Medium At: 48 Inches

Signature:

Alter Va

# **DISCLAIMER**

### Brian L. Humpal, Inc. dba. Midwest Sewer Services, Inspect Minnesota, Midwest Soil Testing Relative to Subsurface Sewage Treatment System (SSTS) Compliance Inspections

- 1. This inspection/report is being performed for only the seller/owner of the property on which the SSTS is located. In such case that another party is paying for the inspection, the contract is between only said party and Brian L. Humpal, Inc.; there is no contract between Brian L. Humpal, Inc. and any other party unless otherwise noted.
- 3. Brian L. Humpal, Inc. has not been retained to warranty, guarantee, or certify the proper functioning of the SSTS for any period of time beyond the date of inspection or into the future. Because of the numerous factors (usage, maintenance, soil characteristics, previous failures, etc.) which may affect the proper operation of an SSTS, as well as the inability of Brian L. Humpal, Inc. to supervise or monitor the use or maintenance of the SSTS, the report shall not be construed as a warranty by Brian L. Humpal, Inc. that the SSTS will function properly for any particular party for any period of time.
- 4. Brian L. Humpal, Inc. is unable to verify the frequency and/or, quality of prior or future maintenance of the SSTS. Maintenance of the tank(s) must be performed through the tanks maintenance hole. The removal of solids from any location other than the maintenance hole is not a compliant method of maintenance. It is strongly recommended that maintenance covers be made accessible to the ground surface to facilitate proper maintenance.
- 5. Minimum Compliance Inspection requirements relative to this inspection and this report include <u>only</u> verification that the SSTS has tank(s) (septic tanks, lift tanks, dosing tanks, stilling tanks, etc.) which are watertight below the designed operating depth, the required separation between the bottom of the subsurface soil distribution medium and seasonally saturated soils, no back-ups of sewage into the dwelling, no discharge of sewage/effluent to the ground surface or surface waters, and no imminent safety hazards. Brian L. Humpal, Inc. does not inspect plumbing or pumps prior to the first SSTS component as these are plumbing components. The performance of exterior pumps and associated components are not inspected as they are considered to be maintenance items. Additionally, no indications relative to compliance with electrical code requirements have been made. It is recommended that any other applicable plumbing, electrical, housing, etc. inspections be performed by a qualified inspection business. Sewage back-up verification is limited to observing the floor drain area and/or the information supplied by the last occupants of the building prior to inspection. Brian L. Humpal, Inc. cannot guarantee that the information given to them by the last occupants of the building prior to inspection relative to back-ups is accurate.
- 4. Certification of this SSTS does not warranty future use beyond the date of the inspection. Any SSTS, old or new, can become hydraulically overloaded or discharge sewage/effluent to the ground surface as a result of more people moving into the house than were previously occupying the house, improper maintenance, heavy usage, leaking plumbing fixtures, groundwater infiltration, tree roots, freezing conditions, surface drainage problems, poor initial design, poor construction practices, or unsuitable materials used in constructing the system; the system can also simply stop working because of its age. An SSTS that has been properly designed and installed, properly maintained, and used in the manner for which the system was designed can be expected to provide service for twenty to twenty-five years on average. Some parts of the SSTS such as alarms, switches, pumps, filters, etc. will most likely have to be repaired or replaced over the lifetime of the system.
- 5. A Compliance Inspection is not meant to be a test or inspection for longevity of the system; a Compliance Inspection is strictly for the purpose of determining if the SSTS is protective of public health and safety, as well as the groundwater at the date and time the inspection was performed. This inspection is not intended to determine if the SSTS was originally designed or installed to past or present MPCA or other Local Government Unit code requirements. This inspection is not intended to determine if the SSTS was designed and/or installed to support the anticipated flow from the building as the use of the building may have changed since the design and construction of the SSTS due to the addition of bedrooms, occupants, etc. In addition, this inspection is not intended to determine the quality of the original SSTS design, the quality of the construction practices used while installing the SSTS, or the quality of the materials used in constructing the SSTS.
- 6. Brian L. Humpal, Inc. cannot guarantee the performance of SSTS products/components such as: gravelless pipe, chamber trenches, effluent filters, tanks, sewage pre-treatment components, piping, etc. Products such as gravelless pipe are no longer approved for installation in the State of Minnesota and may have a significantly reduced performance and/or life expectancy.
- 7. WINTER WORK: By accepting this report, it is understood that inspections conducted during winter months (approximately November 1<sup>st</sup> through April 1<sup>st</sup>) are more difficult to perform because of possible snow cover and/or ground frost. SSTS components such as tanks, maintenance covers, tank inspection pipes, subsurface distribution medium inspection pipes, and soil treatment areas are more difficult or impossible to locate due to snow cover and/or ground frost. In addition, soil borings are more difficult to perform due to snow cover and/or ground frost. Brian L. Humpal, Inc. will attempt to use the same level of standards when performing work during winter periods as when performing work during non-winter periods. However, the recipient of this report understands that because of the aforementioned considerations, the same level of standards may not be possible.
- 8. By accepting this report, the client understands that Brian L. Humpal, Inc. will not be responsible for any monetary damages exceeding the fee for the services provided.

# Subsurface Sewage Treatment Systems Non-transferable Business License

# **Midwest Sewer Services**

License # L2896

License Expires: 12/22/2020

Issued: 11/26/2019

# **Specialty Area(s):**

Installer Maintainer Service Provider Advanced Designer Advanced Inspector

# **Designated Certified Individual(s):**

| Cert #                      | Name                              | Certification Expires:      |
|-----------------------------|-----------------------------------|-----------------------------|
| C5342                       | Brian L Humpal                    | 10/15/2023                  |
|                             | Installer, Maintainer, Serv Prov, | Adv Designer, Adv Inspector |
| C9852 Christopher R Uebe 3) |                                   | 3/4/2021                    |
|                             | Designer, Inspector               |                             |

# MINNESOTA POLLUTION CONTROL AGENCY

520 Lafayette Road North St. Paul, Minnesota 55155-4194

Haig

Nick Haig, Supervisor Certification and Training Unit
