

---



---

## Midwest Sewer Services

---



---

P.O. Box 10853 White Bear Lake, MN 55110  
651-492-7550/Brian@Midwestsoiltesting.com

Brian Humpal  
MPCA Licensed Advanced Inspector

---

### SUBSURFACE SEWAGE TREATMENT SYSTEM (SSTS) COMPLIANCE REPORT

---

**Date:** August 11, 2020

**Time:** 11:00 AM

**Owner:** Tom Feidt

**Inspection Address:** 8395 235<sup>th</sup> St N, Forest Lake, MN 55025

---

### REPORT SUMMARY

I have performed an “MPCA Compliance Inspection” on this system, have reviewed the history of the system with the owner, Tom Feidt, and have reviewed the original design/permit records on file at Washington County. This older system (installed in 1997) consists of two pre-cast septic tanks, a pre-cast lift tank, and mound. Olson’s Sewer Service pumped the septic tanks and lift tank on August 11, 2020.

Predicated on my inspection of the system, my review of the history of the system with the owner, and my review of the original design/permit records, it is my opinion that this system presently meets MPCA minimum compliance inspection requirements.


Midwest Sewer Services have been hired to perform a compliance inspection of this SSTS for compliance with local ordinances pursuant to Minn. Stat. § 115.55 (2013). This compliance inspection covers only the criteria required by Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011). A compliance inspection is an indication of the current compliance status of the system and does not guarantee the performance or longevity of this system beyond the date of inspection, as it is impossible to determine the future performance of any system. Midwest Sewer Services disclaim any use of this compliance inspection beyond determining SSTS compliance pursuant to Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011).

Please contact me should you have any questions.




---

Christopher Uebe




---

Brian Humpal


**Minnesota Pollution  
Control Agency**

 520 Lafayette Road North  
St. Paul, MN 55155-4194

# Compliance Inspection Form

## Existing Subsurface Sewage Treatment Systems (SSTS)

*Doc Type: Compliance and Enforcement*

**Instructions:** Inspection results based on Minnesota Pollution Control Agency (MPCA) requirements and attached forms – additional local requirements may also apply.

For local tracking purposes:

**Submit completed form to Local Unit of Government (LUG) and system owner within 15 days**

### System Status

 System status on date (mm/dd/yyyy): 8/11/2020
 **Compliant – Certificate of Compliance**
*(Valid for 3 years from report date, unless shorter time frame outlined in Local Ordinance.)*
 **Noncompliant – Notice of Noncompliance**
*(See Upgrade Requirements on page 3)*

#### Reason(s) for noncompliance (*check all applicable*)

- Impact on Public Health (*Compliance Component #1*) – *Imminent threat to public health and safety*
- Other Compliance Conditions (*Compliance Component #3*) – *Imminent threat to public health and safety*
- Tank Integrity (*Compliance Component #2*) – *Failing to protect groundwater*
- Other Compliance Conditions (*Compliance Component #3*) – *Failing to protect groundwater*
- Soil Separation (*Compliance Component #4*) – *Failing to protect groundwater*
- Operating permit/monitoring plan requirements (*Compliance Component #5*) – *Noncompliant*

### Property Information

Parcel ID# or Sec/Twp/Range: \_\_\_\_\_

 Property address: 8395 235<sup>th</sup> St N, Forest Lake, MN 55025

 Reason for inspection: Property Transfer

 Property owner: Tom Feidt

 Owner's phone: 651-245-2253
**or**

Owner's representative: \_\_\_\_\_

Representative phone: \_\_\_\_\_

 Local regulatory authority: Washington County

 Regulatory authority phone: 651-430-6655

 Brief system description: Two pre-cast septic tanks, a pre-cast lift tank, and a mound.

Comments or recommendations: \_\_\_\_\_

### Certification

*I hereby certify that all the necessary information has been gathered to determine the compliance status of this system. No determination of future system performance has been nor can be made due to unknown conditions during system construction, possible abuse of the system, inadequate maintenance, or future water usage.*

 Inspector name: Brian Humpal/Christopher Uebe

 Certification number: C5342/C9852

 Business name: Midwest Sewer Services

 License number: L2896

 Inspector signature: 

 Phone number: 651-492-7550

### Necessary or Locally Required Attachments

- Soil boring logs       System/As-built drawing       Forms per local ordinance
- Other information (list): Report Summary, Property Information, Disclaimer, License

Property address: 8395 235th St N, Forest Lake, MN 55025

Inspector initials/Date: 8/11/2020 *BACU***1. Impact on Public Health – Compliance component #1 of 5****Compliance criteria:**

System discharge sewage to the ground surface.	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
--	---

System discharge sewage to drain tile or surface waters.	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
--	---

System cause sewage backup into dwelling or establishment.	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
--	---

**Any "yes" answer above indicates the system is an Imminent Threat to Public Health and Safety.**

Comments/Explanation:

None of the above found.

**Verification method(s):**

- Searched for surface outlet
- Searched for seeping in yard/backup in home
- Excessive ponding in soil system/D-boxes
- Homeowner testimony (See Comments/Explanation)
- "Black soil" above soil dispersal system
- System requires "emergency" pumping
- Performed dye test
- Unable to verify (See Comments/Explanation)
- Other methods not listed (See Comments/Explanation)

**2. Tank Integrity – Compliance component #2 of 5****Compliance criteria:**

System consists of a seepage pit, cesspool, drywell, or leaching pit.	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
---	---

*Seepage pits meeting 7080.2550 may be compliant if allowed in local ordinance.*

Sewage tank(s) leak below their designed operating depth.	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
---	---

If yes, which sewage tank(s) leaks:	
-------------------------------------	--

**Any "yes" answer above indicates the system is Failing to Protect Groundwater.**

Comments/Explanation:

Lowered underwater camera into tanks - baffles and tank walls OK.

Lift pump and alarm were operational at the time of the inspection.

**Verification method(s):**

- Probed tank(s) bottom
- Examined construction records
- Examined Tank Integrity Form (Attach)
- Observed liquid level below operating depth
- Examined empty (pumped) tanks(s)
- Probed outside tank(s) for "black soil"
- Unable to verify (See Comments/Explanation)
- Other methods not listed (See Comments/Explanation)

**3. Other Compliance Conditions – Compliance component #3 of 5**

- a. Maintenance hole covers are damaged, cracked, unsecured, or appear to structurally unsound.  Yes\*  No  Unknown
- b. Other issues (*electrical hazards, etc.*) to immediately and adversely impact public health or safety.  Yes\*  No  Unknown  
**\*System is an imminent threat to public health and safety**

Explain:

- c. System is non-protective of ground water for other conditions as determined by inspector  Yes\*  No  
**\*System is failing to protect groundwater**

Explain:

Property address: 8395 235th St N, Forest Lake, MN 55025

Inspector initials/Date: 8/11/2020 *BACU*

**4. Soil Separation – Compliance component #4 of 5**

Date of installation: 1997  Unknown  
 Shoreland/Wellhead protection/Food Beverage Lodging?  Yes  No

**Compliance criteria:**

For systems built prior to April 1, 1996, and not located in Shoreland or Wellhead Protection Area or not serving a food, beverage or lodging establishment:  Yes  No

Drainfield has at least a two-foot vertical separation distance from periodically saturated soil or bedrock.

Non-performance systems built April 1, 1996, or later or for non-performance systems located in Shoreland or Wellhead Protection Areas or serving a food, beverage, or lodging establishment:  Yes  No

Drainfield has a three-foot vertical separation distance from periodically saturated soil or bedrock.\*

“Experimental”, “Other”, or “Performance” systems built under pre-2008 Rules; Type IV or V systems built under 2008 Rules (7080.2350 or 7080.2400 (Advanced Inspector License required)  Yes  No

Drainfield meets the designed vertical separation distance from periodically saturated soil or bedrock.

**Any “no” answer above indicates the system is Failing to Protect Groundwater.**

**Verification method(s):**

Soil observation does not expire. Previous soil observations by two independent parties are sufficient, unless site conditions have been altered or local requirements differ.

- Conducted soil observation(s) (Attach boring logs)
- Two previous verifications (Attach boring logs)
- Not applicable (Holding tank(s), no drainfield)
- Unable to verify (See Comments/Explanation)
- Other (See Comments/Explanation)

**Comments/Explanation:**

Reviewed design and permit records.

**Indicate depths of elevations**

A. Bottom of distribution media	See Attached Boring Log(s)
B. Periodically saturated soil/bedrock	
C. System separation	
D. Required compliance separation*	

\*May be reduced up to 15 percent if allowed by Local Ordinance.

**5. Operating Permit and Nitrogen BMP\* – Compliance component #5 of 5  Not applicable**

Is the system operated under an Operating Permit?  Yes  No **If “yes”, A below is required**

Is the system required to employ a Nitrogen BMP?  Yes  No **If “yes”, B below is required**

BMP=Best Management Practice(s) specified in the system design

**If the answer to both questions is “no”, this section does not need to be completed.**

**Compliance criteria**

a. Operating Permit number: _____ Have the Operating Permit requirements been met?	<input type="checkbox"/> Yes <input type="checkbox"/> No
b. Is the required nitrogen BMP in place and properly functioning?	<input type="checkbox"/> Yes <input type="checkbox"/> No

**Any “no” answer indicates Noncompliance.**

**Upgrade Requirements** (Minn. Stat. § 115.55) An imminent threat to public health and safety (ITPHS) must be upgraded, replaced, or its use discontinued within ten months of receipt of this notice or within a shorter period if required by local ordinance. If the system is failing to protect ground water, the system must be upgraded, replaced, or its use discontinued within the time required by local ordinance. If an existing system is not failing as defined in law, and has at least two feet of design soil separation, then the system need not be upgraded, repaired, replaced, or its use discontinued, notwithstanding any local ordinance that is more strict. This provision does not apply to systems in shoreland areas, Wellhead Protection Areas, or those used in connection with food, beverage, and lodging establishments as defined in law.

## SSTS MAINTENANCE REPORT

Date of Maintenance 8/11/2000 Reason for Maintenance: 54498519888  
 Property Address: 8395-235th St. N. Property Owner's Name: Thomas Perdt  
 Municipality: Forest Lake State \_\_\_\_\_ Zip Code \_\_\_\_\_ GEO Code/Property I.D. #: \_\_\_\_\_

What was done to the system?	Tank Measurements (must be completed if tanks NOT pumped)
<input checked="" type="checkbox"/> Tank(s) Pumped <input type="checkbox"/> Sludge and scum measured. Do tanks need to be pumped? <input type="checkbox"/> Yes <input type="checkbox"/> No (If no provide measurements)	Liquid Level of Tank _____ in.    Sludge Level _____ in.    Scum Level _____ in. Total (Sludge + Scum) _____ / Liquid Level _____ = % Sludge & Scum _____ *

1. Access used to remove septage:  Maintenance Hole     Other (Go to #3 below)    \* Tank must be pumped if this value is greater than 25%  
 2. If maintenance hole was used, were all covers securely replaced?  Yes     No *please explain*

Explanation: \_\_\_\_\_

3. If owner refuses to allow a Subsurface Sewage Treatment System (SSTS) to be pumped through the maintenance hole, have them complete and sign the following statement:

I, \_\_\_\_\_ (owner's name), refuse to allow the removal of solids and liquids through the maintenance hole. I understand that removal of solids and liquids through other access points is not considered maintenance.

4. Is the tank designed as a leaky tank? *example: seepage pit, cesspool, drywell, leaching pit*

Tank#1     Yes     No    Verificatio Method Used: \_\_\_\_\_

Tank#2     Yes     No    Verificatio Method Used: \_\_\_\_\_

5. Is there evidence of tank leakage from a septic, holding, pretreatment or pump tank below the operating depth or evidence of damaged, cracked, or structurally unsound maintenance hole covers?

Tank	Leaking Out	Leaking In	Cover Damage
Septic/Holding Tank #1	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Septic/Holding Tank #2	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No
Pretreatment Tank	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No	<input type="checkbox"/> Yes <input type="checkbox"/> No
Pump Tank	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No

6. How many gallons of septage were removed?

Tank #1 1500    Tank #2 1000    Pretreatment Tank \_\_\_\_\_    Pump Tank 255

7. Other information: List any troubleshooting, minor repairs conducted, tank safety concerns, or other concerns.  
 \_\_\_\_\_

8. Certification: I hereby certify as a State of Minnesota certified SSTS Maintainer that I personally conducted the work and made the observations, or directly supervised others in the performance of this job.

Maintainer's Name: OSSI    Maintainer's Address: 17638 Lyons St. N.E.

Maintainer's License #: 216    Maintainer's Phone #: 651-464-2082

Maintainer's Signature: [Signature]    Date: 8-11-20

Property address: 8395 235<sup>th</sup> ST NE Parcel ID: \_\_\_\_\_  
City: Forest Lake State: MN Zip code: 55025

### Optional section: Sewage Tank Compliance Certification

This form does not represent a complete system inspection report and only certifies sewage tank compliance status.

**Instructions:** This section of the form may be completed and signed by a Designated Certified Individual (DCI) of a licensed SSTS Maintenance Business who personally conducts the necessary procedures to assess the compliance status of each sewage tank in the system.

When this section of the form is signed by a qualified certified professional, it becomes *necessary supporting documentation* to an Existing System Compliance Inspection Report: Compliance inspection form - Existing system (wq-wwists4-31b). This form can be found on the MPCA website at <https://www.pca.state.mn.us/water/ssts-and-msts-technical-and-compliance-criteria>.

The information and certified statement on this form is **required** when existing septic tank compliance status is determined by an individual other than the SSTS Inspector that submits the inspection report. It represents a third party assessment of SSTS component compliance and is allowable under Minn. R. 7082.0700, subp. 4 Item (B) subitem (1). This form is valid for a period of three years beyond the signature date on this form unless a new evaluation is requested by the owner or owner's agent or is required according to local regulations. Additional Administrative Rule references for this activity can be found at Minn. R. 7082.0700, subp. 4 Items B, C, and D; 7083.0730 Item C.

**Certificate of sewage tank compliance**

Affirm all three statements:

- The SSTS does not contain a seepage pit, cesspool, drywell, leaching pit, or other pit.
- It does not contain a sewage tank that was designed to be watertight, but subsequently leaks below the designed operating depth.
- It does not represent an imminent safety threat by reason of unsecured, damaged, or weak maintenance hole cover(s) or other unsafe condition.

**Notice of sewage tank non-compliance**

Select all that apply:

- The SSTS has a seepage pit, cesspool, drywell, leaching pit, or other pit – **"Failure to Protect Groundwater."**
- It has a sewage tank that was designed to be watertight, but subsequently leaks below the designed operating depth – **"Failure to Protect Groundwater."**
- It presents a threat to public safety by reason of unsecured, damaged, or weak maintenance hole cover(s) or other unsafe condition – **"Imminent Threat to Public Health or Safety."**

**Company information**

Company name: Olson's Sewer

Business license number: \_\_\_\_\_

**Designated Certified Individual (DCI) information**

Print name: Joel Hyden

Certification number: C 6291

I personally conducted the work described above as a Designated Certified Individual of a Minnesota-licensed SSTS Maintenance Business. I personally conducted the necessary procedures to assess the compliance status of each sewage tank in this SSTS:

Designated Certified Individual's signature: Joel Hyden

Date (mm/dd/yyyy): 08/11/2020

7 of 12  
**Midwest Sewer Testing**

**Subsurface Sewage Treatment System Owner/Property Information**

This information will be used for the purpose of conducting an MPCA Compliance Inspection.


Date of Inspection: August 11, 2020		Time: 11:00 AM	
Property Address: 8395 235 <sup>th</sup> St N, Forest Lake MN		Zip: 55025	
Property Owner: Tom Feidt		Phone: 651-245-2253	
Tank(s) <input checked="" type="checkbox"/> Septic 2 <input type="checkbox"/> Aerobic <input checked="" type="checkbox"/> Lift <input type="checkbox"/> Holding <input type="checkbox"/> Other: _____	Tank(s)Material <input type="checkbox"/> Fiberglass <input type="checkbox"/> Plastic <input type="checkbox"/> Metal <input checked="" type="checkbox"/> Concrete <input type="checkbox"/> Block <input type="checkbox"/> Other _____	Soil Treatment System <input type="checkbox"/> Rock trench <input type="checkbox"/> Gravelless trench <input type="checkbox"/> Chamber trench <input type="checkbox"/> Seepage bed <input checked="" type="checkbox"/> Mound <input type="checkbox"/> At-grade _____	Other <input type="checkbox"/> Alternative system _____ <input type="checkbox"/> Experimental system _____ <input type="checkbox"/> Cesspool system _____ <input type="checkbox"/> Other system _____
Are the tank maintenance covers accessible? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No *If no, proper maintenance must be performed through the maintenance holes. Maintenance hole covers should be made accessible to the ground surface to facilitate access and proper maintenance of the system.			
Year house built: 1997	Year septic installed: 1997	Tank size (gals.): 1-1500, 1-1000	
How long has seller owned the property? 1997		Number of residents in home? 2	
Number of bedrooms? 4		Are all floors drained by gravity? Y	
Garbage disposal? N		Whirlpool bath? Y	
More than one system (laundry, etc.)? N			
Does this property have any footing drain tiles connected to the septic system? N			
Are any buildings on this property such as garages or out-buildings connected to this system? N			
Are there any additional systems on this property serving other buildings? N			
Location of septic system on lot? West Side			
Location of water well on lot? North Side		Is the well a deep well? Y	
Have you ever experienced any problems with the system such as: tree roots, sewage back-ups, surfacing of sewage onto the ground, septic tank overflowing, etc.; or have any repairs been made to the system? Y If yes, explain: Replaced pump line and removed roots and tree in approximately 2016/2017.			
When was the system last pumped? 8/11/2020		Name of pumper: Olson's Sewer Service	
How often pumped in previous years? Every 3		Is system on a monitoring plan? N	
Have you received notices from any government agency concerning this system? N			
Is your property located in a shoreland management area? N			
Do you have any additional information that should be given to the new owner? N			

I hereby certify that the above information is correct to the best of my knowledge. I also understand that if the system is considered "non-compliant/failing" per MPCA rules, that the inspector must by law submit a copy of this report to the local government unit within 15 days of the date of inspection completion. I also agree that unless otherwise noted in this report, that I/we are ultimately responsible for payment of all fees for all work performed relative to this inspection by Inspect Minnesota and Midwest Soil Testing

Owner/Occupant: \_\_\_\_\_

Date: \_\_\_\_\_



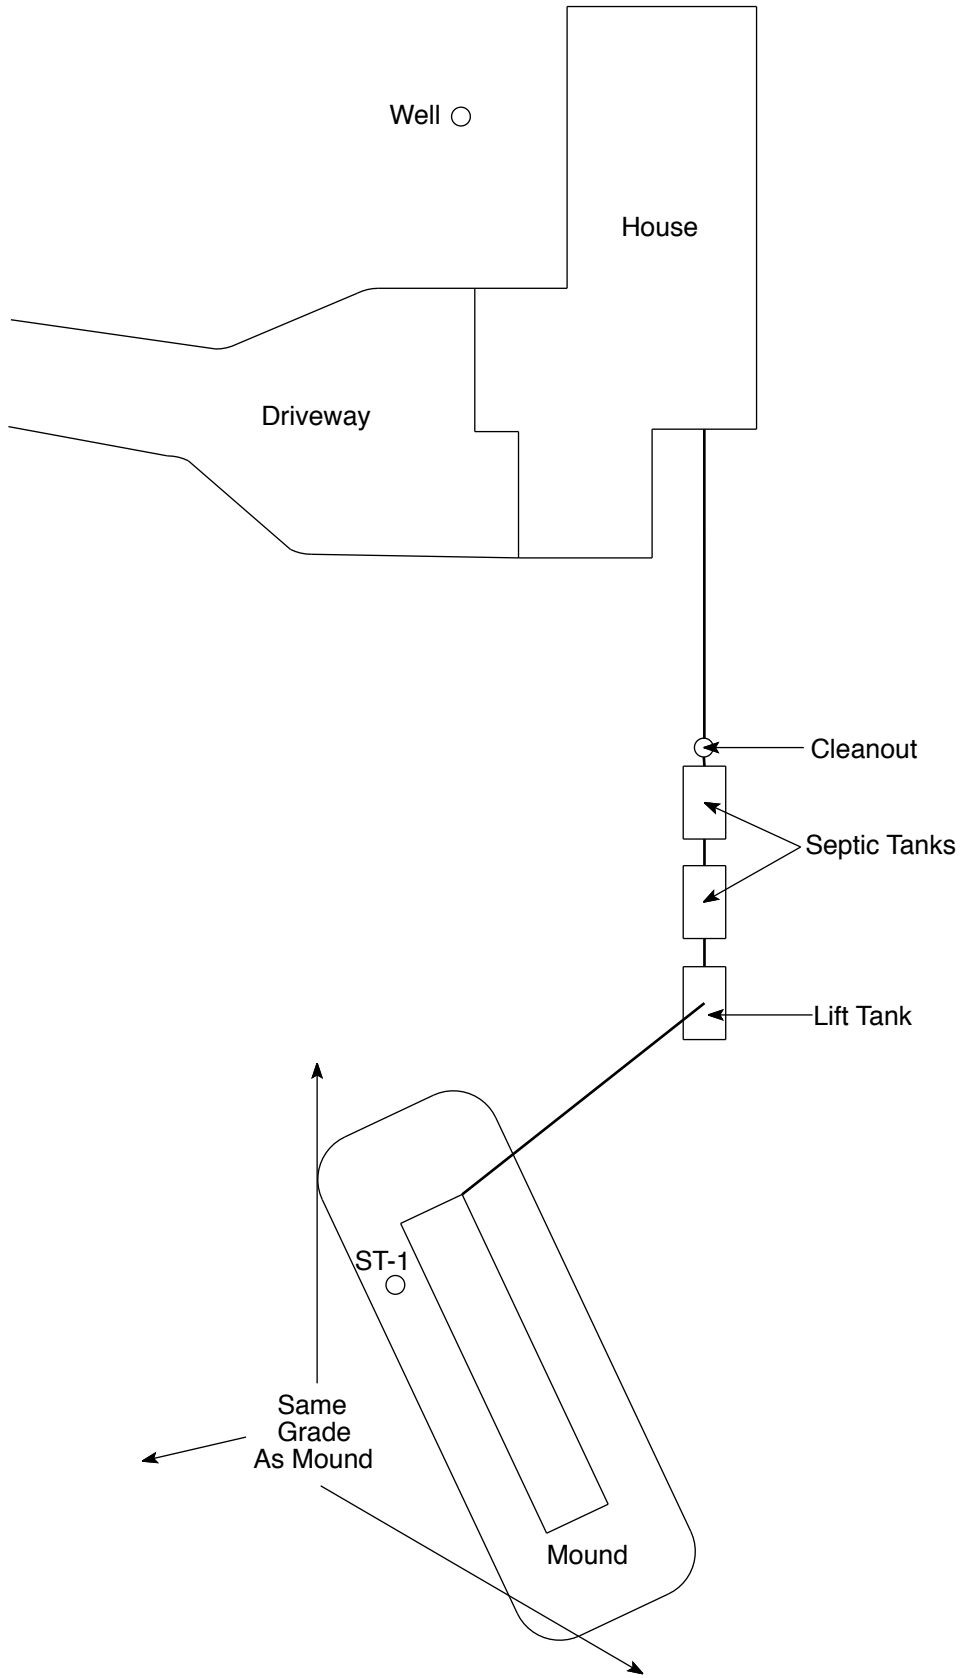

← N  
**NO SCALE**

**8395 235th St N, Forest Lake, MN 55025**



## Soil Observations Log

Location of Project:		8395 235th St N, Forest Lake, MN 55025			
Observations Made By:		Midwest Sewer Services		Date:	8/11/2020
Classification System:		USDA			
Soil Observation:		ST-1		Soil Observation:	
Surface Elevation of Observation				Surface Elevation of Observation	
Depth In Inches	Rock %	<u>Soils Encountered</u>		Depth In Inches	Rock %
0-6		10YR 2/2 Loamy Sand (Fill)			
6-42		10YR 4/4 Medium Sand (Fill)			
42-47		10YR 2/2 Silt Loam (Original Topsoil)			
47-52		10YR 4/3 Fine Loamy Sand			
52-60		10YR 4/3 Clay Loam			
60-65		10YR 4/3 Clay Loam (Moist) With Few 7.5YR 5/8 Redox			
		Due To Lack Of Contour, Soil Boring Was Done Adjacent To Mound Rock Bed To Find Where the Original Depth Of Redox Was			
60"	Depth To End Of Soil Observation Or Redox			Depth To End Of Soil Observation Or Redox	
Same	Elevation Of Observation Below Top Of Mound			Elevation Of Observation Relative To System	
-28"	Depth To Bottom Of Distribution Media			Depth To Bottom Of Distribution Media	
=32"	Of Separation			Of Separation	
End Of Soil Observation At:		65"	End Of Soil Observation At:		
Redox Present At:		60"	Redox Present At:		
Standing Water Present At:		None	Standing Water Present At:		

Bottom Of Distribution Medium At: 28 Inches

---



---

Signature: \_\_\_\_\_





**EARTH SCIENCE TESTING**  
SOILS INFORMATION COMPANY

**SOIL BORINGS**

LOCATION: EXPANDED AREA LOT 1 - BLK 2

**BORING NO. 1-B**

0" - 5" = DARK BROWN FINE SANDY LOAM. (10YR 4/2)  
5" - 16" = BROWN FINE SANDY CLAY LOAM. (10YR 4/4)  
16" - 48" = BROWN FINE SANDY CLAY LOAM, IRON STAINS & MOTTLED.  
VERY STIFF. (10YR 4/4)

END BORE

**BORING NO. 2-B**

0" - 7" = DARK BROWN FINE SANDY LOAM. (10YR 4/2)  
7" - 15" = BROWN FINE SANDY CLAY LOAM. (10YR 4/4)  
15" - 48" = BROWN FINE SANDY CLAY LOAM, IRON STAINS & MOTTLED.  
STIFF. (10YR 4/4)

END BORE

**BORING NO. 3-B**

0" - 9" = DARK BROWN FINE SANDY LOAM. (10YR 4/2)  
9" - 22" = BROWN FINE SANDY CLAY LOAM. (10YR 4/4)  
22" - 48" = LIGHT BROWN FINE SANDY CLAY LOAM, IRON STAINS &  
MOTTLED. (10YR 5/4)

END BORE

**BORING NO. 4-B**

0" - 12" = DARK BROWN FINE SANDY LOAM. (10YR 4/2)  
12" - 26" = LIGHT BROWN FINE SANDY LOAM. (10YR 4/4)  
26" - 48" = LIGHT BROWN FINE SANDY CLAY LOAM, IRON STAINS &  
MOTTLED. (10YR 5/4)

END BORE

**BORING NO. 5-B**

0" - 5" = DARK BROWN FINE SANDY LOAM. (10YR 4/2)  
5" - 12" = BROWN FINE SANDY CLAY LOAM. (10YR 4/4)  
12" - 28" = BROWN FINE SANDY CLAY LOAM, IRON STAINS & MOTTLED.  
VERY STIFF. (10YR 4/4)

END BORE



**EARTH SCIENCE TESTING**  
SOILS INFORMATION COMPANY

**SOIL BORINGS**

JOE PREINER ————— LOT 1 BLK 2

**BORING NO. 1**

0" - 8" DARK BROWN FINE SANDY LOAM  
8" - 13" BROWN FINE SANDY LOAM  
13" - 52" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
52" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRON STAINS,  
—MOTTLES  
6'0" END BORING

**BORING NO. 2**

0" - 12" DARK BROWN FINE SANDY LOAM  
12" - 26" LIGHT BROWN FINE SANDY LOAM  
26" - 49" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
49" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRON STAINS,  
—MOTTLES  
6'0" END BORING

**BORING NO. 3**

0" - 9" DARK BROWN FINE SANDY LOAM  
9" - 60" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
60" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRON STAINS,  
—MOTTLES  
6'0" END BORING

**BORING NO. 4**

0" - 9" DARK BROWN FINE SANDY LOAM  
9" - 22" BROWN FINE SANDY LOAM  
22" - 54" BROWN FINE TO MEDIUM LOAMY SAND  
54" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRON STAINS,  
—MOTTLES  
6'0" END BORING



**EARTH SCIENCE TESTING**  
SOILS INFORMATION COMPANY

**SOIL BORINGS**

JOE PREINER ————— LOT 2 BLK 2

TEST AREA 2

**BORING NO. 1A**

0" - 6" DARK BROWN FINE SANDY LOAM  
6" - 13" BROWN FINE SANDY LOAM  
13" - 40" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
40" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRONSTAINS,  
— MOTTLES  
6'0" END BORING

**BORING NO. 2A**

0" - 12" DARK BROWN FINE SANDY LOAM  
12" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRONSTAINS,  
— MOTTLES  
6'0" END BORING

**BORING NO. 3A**

0" - 8" DARK BROWN FINE SANDY LOAM  
8" - 44" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
44" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRONSTAINS,  
— MOTTLES  
6'0" END BORING

**BORING NO. 4A**

0" - 6" DARK BROWN FINE SANDY LOAM  
6" - 10" LIGHT BROWN FINE SANDY LOAM  
10" - 46" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
46" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRONSTAINS,  
— MOTTLES  
6'0" END BORING

**BORING NO. 5A**

0" - 8" DARK BROWN FINE SANDY LOAM  
8" - 47" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM  
47" - 6'0" LIGHT YELLOW BROWN FINE SANDY CLAY LOAM, IRONSTAINS,  
— MOTTLES  
6'0" END BORING

## **DISCLAIMER**

### Brian L. Humpal, Inc. dba. Midwest Sewer Services, Inspect Minnesota, Midwest Soil Testing Relative to Subsurface Sewage Treatment System (SSTS) Compliance Inspections

1. This inspection/report is being performed for only the seller/owner of the property on which the SSTS is located. In such case that another party is paying for the inspection, the contract is between only said party and Brian L. Humpal, Inc.; there is no contract between Brian L. Humpal, Inc. and any other party unless otherwise noted.
3. Brian L. Humpal, Inc. has not been retained to warranty, guarantee, or certify the proper functioning of the SSTS for any period of time beyond the date of inspection or into the future. Because of the numerous factors (usage, maintenance, soil characteristics, previous failures, etc.) which may affect the proper operation of an SSTS, as well as the inability of Brian L. Humpal, Inc. to supervise or monitor the use or maintenance of the SSTS, the report shall not be construed as a warranty by Brian L. Humpal, Inc. that the SSTS will function properly for any particular party for any period of time.
4. Brian L. Humpal, Inc. is unable to verify the frequency and/or, quality of prior or future maintenance of the SSTS. Maintenance of the tank(s) must be performed through the tanks maintenance hole. The removal of solids from any location other than the maintenance hole is not a compliant method of maintenance. It is strongly recommended that maintenance covers be made accessible to the ground surface to facilitate proper maintenance.
5. Minimum Compliance Inspection requirements relative to this inspection and this report include only verification that the SSTS has tank(s) (septic tanks, lift tanks, dosing tanks, stilling tanks, etc.) which are watertight below the designed operating depth, the required separation between the bottom of the subsurface soil distribution medium and seasonally saturated soils, no back-ups of sewage into the dwelling, no discharge of sewage/effluent to the ground surface or surface waters, and no imminent safety hazards. Brian L. Humpal, Inc. does not inspect plumbing or pumps prior to the first SSTS component as these are plumbing components. The performance of exterior pumps and associated components are not inspected as they are considered to be maintenance items. Additionally, no indications relative to compliance with electrical code requirements have been made. It is recommended that any other applicable plumbing, electrical, housing, etc. inspections be performed by a qualified inspection business. Sewage back-up verification is limited to observing the floor drain area and/or the information supplied by the last occupants of the building prior to inspection. Brian L. Humpal, Inc. cannot guarantee that the information given to them by the last occupants of the building prior to inspection relative to back-ups is accurate.
4. Certification of this SSTS does not warranty future use beyond the date of the inspection. Any SSTS, old or new, can become hydraulically overloaded or discharge sewage/effluent to the ground surface as a result of more people moving into the house than were previously occupying the house, improper maintenance, heavy usage, leaking plumbing fixtures, groundwater infiltration, tree roots, freezing conditions, surface drainage problems, poor initial design, poor construction practices, or unsuitable materials used in constructing the system; the system can also simply stop working because of its age. An SSTS that has been properly designed and installed, properly maintained, and used in the manner for which the system was designed can be expected to provide service for twenty to twenty-five years on average. Some parts of the SSTS such as alarms, switches, pumps, filters, etc. will most likely have to be repaired or replaced over the lifetime of the system.
5. A Compliance Inspection is not meant to be a test or inspection for longevity of the system; a Compliance Inspection is strictly for the purpose of determining if the SSTS is protective of public health and safety, as well as the groundwater at the date and time the inspection was performed. This inspection is not intended to determine if the SSTS was originally designed or installed to past or present MPCA or other Local Government Unit code requirements. This inspection is not intended to determine if the SSTS was designed and/or installed to support the anticipated flow from the building as the use of the building may have changed since the design and construction of the SSTS due to the addition of bedrooms, occupants, etc. In addition, this inspection is not intended to determine the quality of the original SSTS design, the quality of the construction practices used while installing the SSTS, or the quality of the materials used in constructing the SSTS.
6. Brian L. Humpal, Inc. cannot guarantee the performance of SSTS products/components such as: gravelless pipe, chamber trenches, effluent filters, tanks, sewage pre-treatment components, piping, etc. Products such as gravelless pipe are no longer approved for installation in the State of Minnesota and may have a significantly reduced performance and/or life expectancy.
7. WINTER WORK: By accepting this report, it is understood that inspections conducted during winter months (approximately November 1<sup>st</sup> through April 1<sup>st</sup>) are more difficult to perform because of possible snow cover and/or ground frost. SSTS components such as tanks, maintenance covers, tank inspection pipes, subsurface distribution medium inspection pipes, and soil treatment areas are more difficult or impossible to locate due to snow cover and/or ground frost. In addition, soil borings are more difficult to perform due to snow cover and/or ground frost. Brian L. Humpal, Inc. will attempt to use the same level of standards when performing work during winter periods as when performing work during non-winter periods. However, the recipient of this report understands that because of the aforementioned considerations, the same level of standards may not be possible.
8. By accepting this report, the client understands that Brian L. Humpal, Inc. will not be responsible for any monetary damages exceeding the fee for the services provided.

# Subsurface Sewage Treatment Systems

Non-transferable

# Business License

## Midwest Sewer Services

License # L2896

License Expires: 12/22/2020

Issued: 11/26/2019

### Specialty Area(s):

- Installer
- Maintainer
- Service Provider
- Advanced Designer
- Advanced Inspector

### Designated Certified Individual(s):

Cert #	Name	Certification Expires:
C5342	Brian L Humpal Installer, Maintainer, Serv Prov, Adv Designer, Adv Inspector	10/15/2023
C9852	Christopher R Uebe Designer, Inspector	3/4/2021



520 Lafayette Road North  
St. Paul, Minnesota 55155-4194

Nick Haig, Supervisor  
Certification and Training Unit
