Midwest Sewer Services

P.O. Box 10853 White Bea	Brian Humpal						
651-492-7550/Brian@Midw	MPCA Licensed Advanced Inspector						
SUBSURFACE SEWAGE TREATMENT SYSTEM (SSTS) COMPLIANCE REPORT							
Date: March 14, 2022Time: 1:00 PMOwner: Steve Carbone							
Inspection Address: 6647 Crackleberry Ct, Woodbury, MN 55129							

REPORT SUMMARY

I have performed an "MPCA Compliance Inspection" on this system and have reviewed the original design/permit records on file at the City of Woodbury. This system consists of two pre-cast septic tanks and a rock trench drainfield. It should be noted that the average life expectancy of a septic system is approximately 30 years. Pinky's Sewer Service pumped the septic tank on March 14, 2022.

Predicated on my inspection of the system and my review of the original design/permit records, it is my opinion that this system <u>presently meets</u> MPCA minimum compliance inspection requirements.

Midwest Sewer Services have been hired to perform a compliance inspection of this SSTS for compliance with local ordinances pursuant to Minn. Stat. § 115.55 (2013). This compliance inspection covers only the criteria required by Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011). A compliance inspection is an indication of the current compliance status of the system and does not guarantee the performance or longevity of this system beyond the date of inspection, as it is impossible to determine the future performance of any system. Midwest Sewer Services disclaim any use of this compliance inspection beyond determining SSTS compliance pursuant to Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011).

Please contact me should you have any questions.

Christopher Uebe

Brian Humpal

Brian Humpal



520 Lafayette Road North St. Paul, MN 55155-4194

Compliance inspection report form

Existing Subsurface Sewage Treatment System (SSTS)

Doc Type: Compliance and Enforcement

Instructions: Inspector must submit completed form to Local Governmental Unit (LGU) and system owner within 15 days of final determination of compliance or noncompliance. Instructions for filling out this form are located on the Minnesota Pollution Control Agency (MPCA) website at https://www.pca.state.mn.us/sites/default/files/wq-wwists4-31a.pdf.

2 of 10

Property information	Local tracking	number:
Parcel ID# or Sec/Twp/Range:	Reason for Inspection	Property Transfer
Local regulatory authority info: Wasington County		
Property address: <u>6647 Crackleberry Ct, Woodbury, MN 55129</u>		
Owner/representative: Steve Carbone		_ Owner's phone: <u>651-503-1452</u>
Brief system description: Two pre-cast septic tanks and a rock tree	nch drainfield.	

System status

System status on date (mm/dd/yyyy): 3/14/2022

Compliant – Certificate of compliance*

(Valid for 3 years from report date unless evidence of an imminent threat to public health or safety requiring removal and abatement under section 145A.04, subdivision 8 is discovered or a shorter time frame exists in Local Ordinance.)

*Note: Compliance indicates conformance with Minn. R. 7080.1500 as of system status date above and does not guarantee future performance.

□ Noncompliant – Notice of noncompliance

Systems failing to protect ground water must be upgraded, replaced, or use discontinued within the time required by local ordinance.

An imminent threat to public health and safety (ITPHS) must be upgraded, replaced, or its use discontinued within ten months of receipt of this notice or within a shorter period if required by local ordinance or under section 145A.04 subdivision 8.

Reason(s) for noncompliance (check all applicable)

Impact on public health (Compliance component #1) – Imminent threat to public health and safety

Tank integrity (Compliance component #2) – Failing to protect groundwater

Other Compliance Conditions (Compliance component #3) – Imminent threat to public health and safety

Other Compliance Conditions (Compliance component #3) – Failing to protect groundwater

System not abandoned according to Minn. R. 7080.2500 (Compliance component #3) – Failing to protect groundwater

Soil separation (Compliance component #5) - Failing to protect groundwater

Operating permit/monitoring plan requirements (Compliance component #4) – Noncompliant - local ordinance applies

Comments or recommendations

Certification

I hereby certify that all the necessary information has been gathered to determine the compliance status of this system. No determination of future system performance has been nor can be made due to unknown conditions during system construction, possible abuse of the system, inadequate maintenance, or future water usage.

By typing my name below, I certify the above statements to be true and correct, to the best of my knowledge, and that this information can be used for the purpose of processing this form.

 Business name:
 Midwest Sewer Services
 Certification number: 5342/9852

 Inspector signature:
 Brian Humpal
 Hum Humpal
 License number: L2896

 (This document has been electronically signed)
 Phone: 651-492-7550

 Necessary or locally required supporting documentation (must be attached)

Soil observation logs System/As-Built Locally required forms Tank Integrity Assessment Operating Permit Other information (list): Report Summary, Property Information, Disclaimer

Property Address: 6647 Crackleberry Ct, Woodbury, MN 55129

Business Name: Midwest Sewer Services

Date: 3/14/2022

1. Impact on public health – Compliance component #1 of 5

Compliance criteria:		Attached supporting documentation:		
System discharges sewage to the ground surface	🗆 Yes* 🛛 No	☐ Other: ☐ Not applicable		
System discharges sewage to drain tile or surface waters.	🗌 Yes* 🛛 No			
System causes sewage backup into dwelling or establishment.	🗌 Yes* 🛛 No			
Any "yes" answer above indicates imminent threat to public health an				
Describe verification methods and	results:			

None of the above found.

2. Tank integrity – Compliance component #2 of 5

Compliance criteria:		Attached supporting d	ocumentation:	
System consists of a seepage pit,	🗌 Yes* 🛛 No	Empty tank(s) viewed by inspector		
cesspool, drywell, leaching pit, or other pit?		Name of maintenance t	Pinky's Sewer Service	
Sewage tank(s) leak below their	🗌 Yes* 🛛 No	License number of mair	ntenance busines	s: <u>L1673</u>
designed operating depth?		Date of maintenance:	3/14/2022	
		Existing tank integrity assessment (Attach)		
		Date of maintenance		
If yes, which sewage tank(s) leaks:	_	(mm/dd/yyyy): (must be within three years		three years)
Any "yes" answer above indic is failing to protect groundwat	-	(See form instructions to Minn. R. 7082.0700 sub		nent complies with
		🗌 Tank is Noncompliant (oumping not necess	ary – explain below)
		Other:		

Describe verification methods and results:

٠

4 of 10

Property Address:	6647 Crackleberry Ct, Woodbury, MN 55129
Business Name:	Midwest Sewer Services

Date: 3/14/2022

3. Other compliance conditions – Compliance component #3 of 5

	За.	Maintenance hole covers appear to be structurally unsound (damaged, cracked, etc.), or unsect	ured?	
		□ Yes* ⊠ No □ Unknown		
	3b.	Other issues (electrical hazards, etc.) to immediately and adversely impact public health or safety?	? 🗌 Yes*	🖾 No 🔲 Unknown
		*Yes to 3a or 3b - System is an imminent threat to public health and safety.		
	3c.	System is non-protective of ground water for other conditions as determined by inspector?	□ Yes*	🖾 No
	3d.	System not abandoned in accordance with Minn. R. 7080.2500?	□ Yes*	🖾 No
		*Yes to 3c or 3d - System is failing to protect groundwater.		
		Describe verification methods and results:		
		Attached supporting documentation: 🛛 Not applicable		
4.	Ор	erating permit and nitrogen BMP* – Compliance component #4 of	5 🛛 N	ot applicable
	Is th	e system operated under an Operating Permit?	"yes", A	below is required
	Is th	e system required to employ a Nitrogen BMP specified in the system design? Yes No If	"yes", B	below is required
		BMP = Best Management Practice(s) specified in the system design		

If the answer to both questions is "no", this section does not need to be completed.

Compliance criteria:

a. Have the operating permit requirements been met?

b. Is the required nitrogen BMP in place and properly functioning?

Any "no" answer indicates noncompliance.

Describe verification methods and results:

Attached supporting documentation: Operating permit (Attach)

5 of	10	
------	----	--

Property Address:	6647 Crackleberry Ct, Woodbury, MN 55129
Business Name:	Midwest Sewer Services

5. Soil separation – Compliance component #5 of 5

Date of installation 1992 (mm/dd/yyyy)	_ 🗌 Unknown	
Shoreland/Wellhead protection/Food beverage lodging?	🛛 Yes 🗌	Soil observation logs completed for the report
Compliance criteria (select one): 5a. For systems built prior to April 1, 1996, and not located in Shoreland or Wellhead Protection Area or not serving a food, beverage or lodging establishment:	Yes It	 Two previous verifications of required vertical separation Not applicable (No soil treatment area) Reviewed design and permit records. Wellhead protection area.
Drainfield has at least a two-foot vertical separation distance from periodically saturated soil or bedrock.		
 5b. Non-performance systems built April 1, 1996, or later or for non- performance systems located in Shoreland or Wellhead Protection Areas or serving a food, beverage, or lodging establishment: Drainfield has a three-foot vertical separation distance from periodically saturated soil or bedrock.* 	⊠ Yes □ t	Indicate depths or elevations A. Bottom of distribution media See Attached Boring Log(s) B. Periodically saturated soil/bedrock C. System separation D. Required compliance separation* *May be reduced up to 15 percent if allowed by Local Ordinance.
5c. "Experimental", "Other", or "Performance" systems built under pre-2008 Rules; Type IV or V systems built under 2008 Rules 7080. 2350 or 7080.2400 (Intermediate Inspector License required ≤ 2,500 gallons per day; Advanced Inspector License required > 2,500 gallons per day) Drainfield meets the designed vertical separation distance from periodically saturated soil or bedrock.	☐ Yes ☐ M	o*

*Any "no" answer above indicates the system is failing to protect groundwater.

Describe verification methods and results:

Upgrade requirements: (Minn. Stat. § 115.55) An imminent threat to public health and safety (ITPHS) must be upgraded, replaced, or its use discontinued within ten months of receipt of this notice or within a shorter period if required by local ordinance. If the system is failing to protect ground water, the system must be upgraded, replaced, or its use discontinued within the time required by local ordinance. If an existing system is not failing as defined in law, and has at least two feet of design soil separation, then the system need not be upgraded, replaced, or its use discontinued, notwithstanding any local ordinance that is more strict. This provision does not apply to systems in shoreland areas, Wellhead Protection Areas, or those used in connection with food, beverage, and lodging establishments as defined in law.

Midwest Sewer Testing

Subsurface Sewage Treatment System Owner/Property Information


This information will be used for the purpose of conducting an MPCA Compliance Inspection.

Date of Inspection: March 14, 2022	Time: 1:00 PM						
Property Address: 6647 Crackleberry Ct, Woodbury, MN	Zip: 55129						
Property Owner: Steve Carbone	Phone: 651-503-1452						
Tank(s)Tank(s)MaterialSoil Treatment SystemSeptic 2FiberglassRock trenchAerobicPlasticGravelless trenchLiftMetalChamber trenchHoldingConcreteSeepage bedOther:BlockMound	Other Alternative system Experimental system Cesspool system Other system						
☐Other ☐At-grade Are the tank maintenance covers accessible? ⊠ Yes ☐ No *If performed through the maintenance holes. Maintenance hole cov the ground surface to facilitate access and proper maintenance of	ers should be made accessible to the system.						
Year house built: 1992Year septic installed: 1992							
	esidents in home?						
Number of bedrooms?4Are all floors drained by g	ravity? Y						
Garbage disposal? Whirlpool bath?	?						
More than one system (laundry, etc.)?							
Does this property have any footing drain tiles connected to the septic system? Are any buildings on this property such as garages or out-buildings connected to this system?							
Are there any additional systems on this property serving other bu	Are there any additional systems on this property serving other buildings?						
Location of septic system on lot? South Side							
Location of water well on lot? Is the	e well a deep well? Y						
Have you ever experienced any problems with the system such as: tree roots, sewage back-ups, surfacing of sewage onto the ground, septic tank overflowing, etc.; or have any repairs been made to the system? If yes, explain:							
When was the system last pumped? 3/14/2022 Name of pum	nper: Pinky's Sewer Service						
	n on a monitoring plan?						
Have you received notices from any government agency concerning this system?							
Is your property located in a shoreland management area? N							
Do you have any additional information that should be given to the new owner?							

I hereby certify that the above information is correct to the best of my knowledge. I also understand that if the system is considered "non-compliant/failing" per MPCA rules, that the inspector must by law submit a copy of this report to the local government unit within 15 days of the date of inspection completion. I also agree that unless otherwise noted in this report, that I/we are ultimately responsible for payment of all fees for all work performed relative to this inspection by Inspect Minnesota and Midwest Soil Testing

Owner/Occupant:



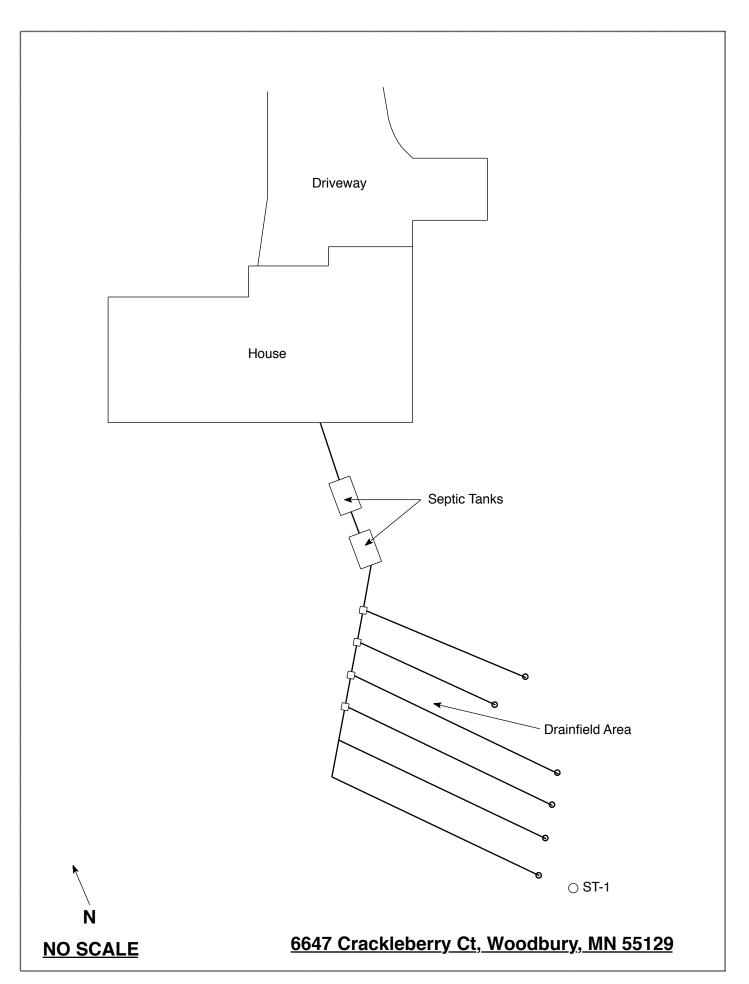

Soil Observations Log

Location of Project: 6647 Crackleberry Ct, Woodbury, MN 55129							
Ot			Midwest Sewer Ser			Date:	3/14/2022
C	lassific	ation System:	USDA				
	Soil	Observation:	ST-1		Soil C	bservation:	
Surf Elevat Obser	ion of	-	nd surface as last field trench	Elevat	Surface Elevation of Observation		
Depth In Inches	Rock %	<u>Soils E</u>	ncountered	Depth In Inches	Rock %	<u>Soils</u>	Encountered
0-2 2-14 14-18 18-27 27-58	≈25 ≈15	10YR 3 10YR 4 10YR 3/4 Sand	2/2 Silt Loam 3/4 Silt Loam 4/4 Silt Loam dy Loam With Gravel um Sand With Gravel				
58"	Depth T	o End Of Soil O	bservation Or Redox		Depth T	o End Of Soil (Observation Or Redox
Same	Elevatio	n Of Observatio	n Relative To System		Elevatio	n Of Observati	on Relative To System
-24"	Depth T	o Bottom Of Dis	stribution Media		Depth T	o Bottom Of D	istribution Media
					Of Sepa		
		Observation At:	58"			servation At:	
		Conditions At:	None	Limiting Soil Conditions At:			
Stan	Standing Water Present At: None Standing Water Present At:						

Bottom Of Distribution Medium At: 24 Inches

Signature:

Afren Va

Logs of Soil Borings B-31 Location or Project _. Wild Canyon Ridge Lot 1 Blick 1 7-28-92 Borings made by Jewy ULFF Date Classification System: AASHO ____; USDA-SCS _L_; Unified ____; other ____ Auger used (check two): Hand _____; or Power ___; Flight ____, or Bucket ____; other Boring number _____BI Boring number ______ Depth, Depth, 96'5 " in 1.n Surface elevation 936" Surface elevation feet feet 0 ---0 -Brown Loam, moist Brown Loam moist 7". 8" Light Brown Loam, moist 1-Light brown Loam, moilt 18" vocks Light Brown medium to 2 ----2 28 Coarse grain Lowing sund. Light Brown medium to coarsie grain Loamy Sand; moist, moist , rocks <u>م</u> rocks Light Iron stady below 4/12 fest. 52 !! Light Brown Fire to Medium ξ...... 5 ----gruin Sand , rocks , moist 68 6 -Obstruction 80 obstruction 7 7 — 8 incles .. End of boring at _5 18 End of boring at <u>BO</u> int Freet. eet. Standing water table: Standing water table: Present at _____ feet of depth, Present at _____ feet of depth, hours after boring. _____ hours after boring. Not present in boring hole Not present in boring hole Mottled soil: Mottled soil: · Observed at _____ feet of depth. Observed at _____ feet of depth. Not present in boring hole 上 Not present in boring hole Observations and comments: Observations and comments:

9 of 10

DISCLAIMER

Brian L. Humpal, Inc. dba. Midwest Sewer Services, Inspect Minnesota, Midwest Soil Testing Relative to Subsurface Sewage Treatment System (SSTS) Compliance Inspections

- 1. This inspection/report is being performed for only the seller/owner of the property on which the SSTS is located. In such case that another party is paying for the inspection, the contract is between only said party and Brian L. Humpal, Inc.; there is no contract between Brian L. Humpal, Inc. and any other party unless otherwise noted.
- 3. Brian L. Humpal, Inc. has not been retained to warranty, guarantee, or certify the proper functioning of the SSTS for any period of time beyond the date of inspection or into the future. Because of the numerous factors (usage, maintenance, soil characteristics, previous failures, etc.) which may affect the proper operation of an SSTS, as well as the inability of Brian L. Humpal, Inc. to supervise or monitor the use or maintenance of the SSTS, the report shall not be construed as a warranty by Brian L. Humpal, Inc. that the SSTS will function properly for any particular party for any period of time.
- 4. Brian L. Humpal, Inc. is unable to verify the frequency and/or, quality of prior or future maintenance of the SSTS. Maintenance of the tank(s) must be performed through the tanks maintenance hole. The removal of solids from any location other than the maintenance hole is not a compliant method of maintenance. It is strongly recommended that maintenance covers be made accessible to the ground surface to facilitate proper maintenance.
- 5. Minimum Compliance Inspection requirements relative to this inspection and this report include <u>only</u> verification that the SSTS has tank(s) (septic tanks, lift tanks, dosing tanks, stilling tanks, etc.) which are watertight below the designed operating depth, the required separation between the bottom of the subsurface soil distribution medium and seasonally saturated soils, no back-ups of sewage into the dwelling, no discharge of sewage/effluent to the ground surface or surface waters, and no imminent safety hazards. Brian L. Humpal, Inc. does not inspect plumbing or pumps prior to the first SSTS component as these are plumbing components. The performance of exterior pumps and associated components are not inspected as they are considered to be maintenance items. Additionally, no indications relative to compliance with electrical code requirements have been made. It is recommended that any other applicable plumbing, electrical, housing, etc. inspections be performed by a qualified inspection business. Sewage back-up verification is limited to observing the floor drain area and/or the information supplied by the last occupants of the building prior to inspection. Brian L. Humpal, Inc. cannot guarantee that the information given to them by the last occupants of the building prior to inspection relative to back-ups is accurate.
- 4. Certification of this SSTS does not warranty future use beyond the date of the inspection. Any SSTS, old or new, can become hydraulically overloaded or discharge sewage/effluent to the ground surface as a result of more people moving into the house than were previously occupying the house, improper maintenance, heavy usage, leaking plumbing fixtures, groundwater infiltration, tree roots, freezing conditions, surface drainage problems, poor initial design, poor construction practices, or unsuitable materials used in constructing the system; the system can also simply stop working because of its age. An SSTS that has been properly designed and installed, properly maintained, and used in the manner for which the system was designed can be expected to provide service for twenty to twenty-five years on average. Some parts of the SSTS such as alarms, switches, pumps, filters, etc. will most likely have to be repaired or replaced over the lifetime of the system.
- 5. A Compliance Inspection is not meant to be a test or inspection for longevity of the system; a Compliance Inspection is strictly for the purpose of determining if the SSTS is protective of public health and safety, as well as the groundwater at the date and time the inspection was performed. This inspection is not intended to determine if the SSTS was originally designed or installed to past or present MPCA or other Local Government Unit code requirements. This inspection is not intended to determine if the SSTS was designed and/or installed to support the anticipated flow from the building as the use of the building may have changed since the design and construction of the SSTS due to the addition of bedrooms, occupants, etc. In addition, this inspection is not intended to determine the quality of the original SSTS design, the quality of the construction practices used while installing the SSTS, or the quality of the materials used in constructing the SSTS.
- 6. Brian L. Humpal, Inc. cannot guarantee the performance of SSTS products/components such as: gravelless pipe, chamber trenches, effluent filters, tanks, sewage pre-treatment components, piping, etc. Products such as gravelless pipe are no longer approved for installation in the State of Minnesota and may have a significantly reduced performance and/or life expectancy.
- 7. WINTER WORK: By accepting this report, it is understood that inspections conducted during winter months (approximately November 1st through April 1st) are more difficult to perform because of possible snow cover and/or ground frost. SSTS components such as tanks, maintenance covers, tank inspection pipes, subsurface distribution medium inspection pipes, and soil treatment areas are more difficult or impossible to locate due to snow cover and/or ground frost. In addition, soil borings are more difficult to perform due to snow cover and/or ground frost. Brian L. Humpal, Inc. will attempt to use the same level of standards when performing work during winter periods as when performing work during non-winter periods. However, the recipient of this report understands that because of the aforementioned considerations, the same level of standards may not be possible.
- 8. By accepting this report, the client understands that Brian L. Humpal, Inc. will not be responsible for any monetary damages exceeding the fee for the services provided.
