1 of 9

Inspect Minnesota & Midwest Soil Testing

P.O. Box 10853 White Bear L	ake, MN 55110	Brian Humpal
651-492-7550/Brian@Midwes	tsoiltesting.com	MPCA Licensed Advanced Inspector
SUBSURFACE SEWAGE TR	REATMENT SYSTEM	I (SSTS) COMPLIANCE REPORT
Date: September 10, 2019	Time: 3:30 PM	Owner: Robert Golden
Inspection Address: 8475 Hidde	en Bay Trail N, Lake Eln	no, MN 55042

REPORT SUMMARY

I have performed an "MPCA Compliance Inspection" on this system, have reviewed the history of the system with the owner, Robert Golden, and have reviewed the original design/permit records on file at Washington County. This system consists of two pre-cast septic tanks, a pre-cast lift tank, and a rock trench drainfield.

Predicated on my inspection of the system, my review of the history of the system with the owner, and my review of the original design/permit records, it is my opinion that this system <u>presently meets</u> MPCA minimum compliance inspection requirements.

Inspect Minnesota and Midwest Soil Testing have been hired to perform a compliance inspection of this SSTS for compliance with local ordinances pursuant to Minn. Stat. § 115.55 (2013). This compliance inspection covers only the criteria required by Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011). A compliance inspection is an indication of the current compliance status of the system and does not guarantee the performance or longevity of this system beyond the date of inspection, as it is impossible to determine the future performance of any system. Inspect Minnesota and Midwest Soil Testing disclaim any use of this compliance inspection beyond determining SSTS compliance pursuant to Minn. Stat. § 115.55 Subd. 5a (2013) and Minn. R. 7080.1500 (2011).

Please contact me should you have any questions.

Christopher Uebe

Brian Humpal

Brian Humpal

Minnesota Pollution Control Agency	Compliar
520 Lafayette Road North St. Paul, MN 55155-4194	Existing Subsurf

Compliance Inspection Form

Existing Subsurface Sewage Treatment Systems

(SSTS)

Doc Type: Compliance and Enforcement

Instructions: Inspection results based on Minnesota Pollution Control Agency (MPCA)	For local tracking purposes:
requirements and attached forms – additional local requirements may also apply.	

Submit completed form to Local Unit of Government (LUG) and system owner within 15 days

System Status

System status on date (mm/dd/yyyy): _____9/10/2019

Compliant – Certificate of Compliance

(Valid for 3 years from report date, unless shorter time frame outlined in Local Ordinance.)

Noncompliant – Notice of Noncompliance

(See Upgrade Requirements on page 3)

Reason(s) for noncompliance (check all applicable)

Impact on Public Health (Compliance Component #1) – Imminent threat to public health and safety

Other Compliance Conditions (Compliance Component #3) – Imminent threat to public health and safety

Tank Integrity (Compliance Component #2) – Failing to protect groundwater

Other Compliance Conditions (Compliance Component #3) – Failing to protect groundwater

Soil Separation (Compliance Component #4) – Failing to protect groundwater

Operating permit/monitoring plan requirements (Compliance Component #5) – Noncompliant

Property Information

Parcel ID# or Sec/Twp/Range:

Property address:	8475 H	idden Bay Trail N, Lake Elmo, MN 55042	Reason for inspection:	Property Transfer			
Property owner:	rty owner:Robert Golden		Owner's phone:				
or							
Owner's represen	tative:		Representative phone:				
Local regulatory a	uthority:	Washington County	Regulatory authority pho	ne: 651-430-6655			
Brief system desc	ription:	Two pre-cast septic tanks, a pre-cast lift tank, ar	nd a rock trench drainfield				
Comments or reco	ommenda	tions:					

Certification

I hereby certify that all the necessary information has been gathered to determine the compliance status of this system. No determination of future system performance has been nor can be made due to unknown conditions during system construction, possible abuse of the system, inadequate maintenance, or future water usage.

Inspector name:	Brian Humpal	/Christopher Uebe	Certification number:	C5342/C9852
Business name:	Inspect Minne	sota, Midwest Soil Testing	License number:	L2896
Inspector signatur	e:	ian Humpal After Va	Phone number:	651-492-7550
Necessary or	Locally Re	quired Attachments		
🛛 Soil boring lo	ogs [System/As-built drawing	Forms per local ordinal	nce
I Other inform	ation (list):R	eport Summary, Property Informa	tion, Disclaimer, License	

2 of 9

1. Impact on Public Health – Compliance component #1 of 5

Property address: 8475 Hidden Bay Trail N, Lake Elmo, MN 55042

Compliance criteria: Verification method(s): Searched for surface outlet System discharge sewage to the □ Yes ⊠ No Searched for seeping in yard/backup in home ground surface. Excessive ponding in soil system/D-boxes □Yes ⊠No System discharge sewage to drain tile Homeowner testimony (See Comments/Explanation) or surface waters. "Black soil" above soil dispersal system □ Yes ⊠ No System cause sewage backup into System requires "emergency" pumping dwelling or establishment. Performed dye test Any "yes" answer above indicates the system is Unable to verify (See Comments/Explanation) an Imminent Threat to Public Health and Safety. Other methods not listed (See Comments/Explanation)

Comments/Explanation:

None of the above found.

2.

Tank Integrity – Compliance component #2 of 5

Verification method(s):

Examined construction records
 Examined Tank Integrity Form (Attach)
 Observed liquid level below operating depth

Examined empty (pumped) tanks(s)
 Probed outside tank(s) for "black soil"
 Unable to verify (See Comments/Explanation)

Other methods not listed (See Comments/Explanation)

Compliance criteria:	
System consists of a seepage pit, cesspool, drywell, or leaching pit.	🗌 Yes 🖾 No
Seepage pits meeting 7080.2550 may be compliant if allowed in local ordinance.	
Sewage tank(s) leak below their designed operating depth.	🗌 Yes 🖾 No
If yes, which sewage tank(s) leaks:	

Any "yes" answer above indicates the system is Failing to Protect Groundwater.

Comments/Explanation:

Lowered underwater camera into tanks - baffles and tank walls OK. Lift pump and alarm were operational at the time of the inspection.

3. Other Compliance Conditions - Compliance component #3 of 5

a. Maintenance hole covers are damaged, cracked, unsecured, or appear to structurally unsound. 🗌 Yes* 🖾 No	
--	--

b. Other issues (electrical hazards, etc.) to immediately and adversely impact public health or safety. \Box Yes* \boxtimes No \Box Unknown *System is an imminent threat to public health and safety

Explain:

c. System is non-protective of ground water for other conditions as determined by inspector Yes* No *System is failing to protect groundwater

Explain:

4. Soil Separation – Compliance component #4 of 5

Date of installation: 2014	Unknown	Verification method(s):			
Shoreland/Wellhead protection/Food Beverage Lodging?	🛛 Yes 🗌 No	Soil observation does not expire. Previous soil observations by two independent parties are suffici			
Compliance criteria:		unless site conditions have been al			
For systems built prior to April 1, 1996, and not located in Shoreland or Wellhead Protection Area or not serving a food, beverage or lodging establishment: Drainfield has at least a two-foot vertical separation distance from periodically saturated soil or bedrock.	☐ Yes ☐ No	 requirements differ. Conducted soil observation(s) (A Two previous verifications (Attain Not applicable (Holding tank(s), n Unable to verify (See Comments/ Other (See Comments/Explanation) 	ch boring logs) o drainfield) Æxplanation)		
Non-performance systems built April 1, 1996, or later or for non-performance systems located in Shoreland or Wellhead Protection Areas or serving a food, beverage, or lodging establishment:	🖾 Yes 🗌 No	<i>Comments/Explanation:</i> Reviewed design and permit records.			
Drainfield has a three-foot vertical separation distance from periodically saturated soil or bedrock.*					
"Experimental", "Other", or "Performance"	🗌 Yes 🔲 No	Indicate depths of elevations			
systems built under pre-2008 Rules; Type IV or V systems built under 2008 Rules (7080. 2350 or 7080.2400 (Advanced Inspector License required)		A. Bottom of distribution media	See Attached Boring Log(s)		
Drainfield meets the designed vertical		B. Periodically saturated soil/bedrock			
separation distance from periodically saturated soil or bedrock.		C. System separation			
		D. Required compliance separation*			
Any "no" answer above indicates the Failing to Protect Groundwater.	he system is	*May be reduced up to 15 percent i Ordinance.	f allowed by Loca		
Operating Permit and Nitrogen B	MP* – Complianc	e component #5 of 5 🛛 🛛 Not app	licable		
Is the system operated under an Operating Per	mit? 🗌 Yes	□ No If "yes", A below is required			
Is the system required to employ a Nitrogen BN	IP? 🗌 Yes	□ No If "yes", B below is required			
BMP=Best Management Practice(s) specif	ied in the system de	sign			
If the answer to both questions is "no",	this section does	s not need to be completed.			

Compliance criteria

a.	Operating Permit number:	🗌 Yes 🗌 No
	Have the Operating Permit requirements been met?	
b.	Is the required nitrogen BMP in place and properly functioning?	🗌 Yes 🗌 No

Any "no" answer indicates Noncompliance.

Upgrade Requirements (Minn. Stat. § 115.55) An imminent threat to public health and safety (ITPHS) must be upgraded, replaced, or its use discontinued within ten months of receipt of this notice or within a shorter period if required by local ordinance. If the system is failing to protect ground water, the system must be upgraded, replaced, or its use discontinued within the time required by local ordinance. If an existing system is not failing as defined in law, and has at least two feet of design soil separation, then the system need not be upgraded, replaced, or its use discontinued, notwithstanding any local ordinance that is more strict. This provision does not apply to systems in shoreland areas, Wellhead Protection Areas, or those used in connection with food, beverage, and lodging establishments as defined in law.

Inspect Minnesota & Midwest Soil Testing

Subsurface Sewage Treatment System Owner/Property Information


This information will be used for the purpose of conducting an MPCA Compliance Inspection.

Date of Inspection: September 10, 2019	Time: 3:30 PM
Property Address: 8475 Hidden Bay Trail N, Lal	xe Elmo, MN Zip: 55042
Property Owner: Robert Golden	Phone:
1 5	reatment System Other
	ck trench Alternative system
	welless trench Experimental system
	amber trench Cesspool system
	page bed Other system und
	grade
Are the tank maintenance covers accessible? \boxtimes Y	es □No *If no, proper maintenance must be
performed through the maintenance holes. Maintenance holes.	
the ground surface to facilitate access and proper	
Year house built: 1959 Year septic installe	d: 2014 Tank size (gals.): 1-1500, 1-1000
1	Number of residents in home? 2-3
	ors drained by gravity? Y
	Whirlpool bath? N
More than one system (laundry, etc.)? N	•
Does this property have any footing drain tiles con	nnected to the septic system? N
Are any buildings on this property such as garages	s or out-buildings connected to this system? N
	<u> </u>
Ano there are additional systems on this monorty	age vin a sthen havildin as 2 M
Are there any additional systems on this property	serving other buildings? IN
Location of septic system on lot? Southeast Side	
Location of water well on lot? North Side	Is the well a deep well? Y
Have you ever experienced any problems with the	
surfacing of sewage onto the ground, septic tank of	
to the system? N If yes, explain:	
When was the system last pumped? 2017	Name of pumper: Meyer Sewer Service
How often pumped in previous years? Every 3	Is system on a monitoring plan? N
Have you received notices from any government a	
Is your property located in a shoreland manageme	
Do you have any additional information that shou	ld be given to the new owner? N

I hereby certify that the above information is correct to the best of my knowledge. I also understand that if the system is considered "non-compliant/failing" per MPCA rules, that the inspector must by law submit a copy of this report to the local government unit within 15 days of the date of inspection completion. I also agree that unless otherwise noted in this report, that I/we are ultimately responsible for payment of all fees for all work performed relative to this inspection by Inspect Minnesota and Midwest Soil Testing.

Owner/Occupant: Robert Golden's Signature On File

Date: 9/10/2019

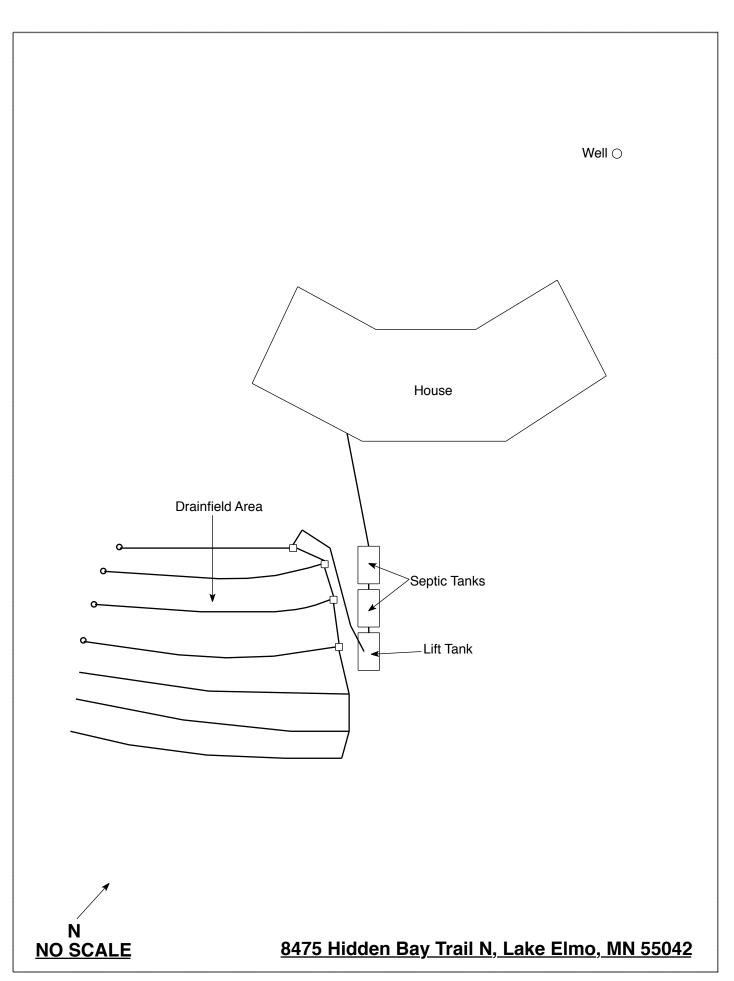

	COMMERCIAL EST. FBL ESTABLISHME		NEW EXISTING DWELLIN		SE ONLY	Ο ΥΤΝΟΟ						TE EVA
	IN WELLHEAD PRO		-SHORELA					gorac	r Gi	276	DRESS:	ROPERTY AL
							50	TIME: JEC			15/1	ATE: 81
					REVIEW	SOIL	_				- /	
			ad	MATERIAL:	PARENT MAT		~	ek?15	Chat		CATION:	DIL CLASSIF
	G 2	SOIL BORIN	J-J *	$\omega \pi$	- 0		_	4G 1	OIL BORN	sc		
	LOCATION:		ING:	ON OF BOR	ELEVATION			LOCATION:	fren	ert	F BORING: C	LEVATION O
	LON:				GPS COORDI			LON:		ю. Ха	ATES: LAT:	S COORDIN
PROBE	PIT	vger 🛛	16 4 7A	PI BORIN	SOIL HORIZON	PROBE		PIT	y~ □	they	BORING φ'	AT.
FEATURES	STRUCTURE	COLOR	TURE	N) TE	DEPTH (IN)	FEATURES	L'	STRUCTURE	COLOR		TEXTURE	DEPTH (IN)
						\mathcal{N}		Gran	1	10	Janes 10m	>-12
						\mathcal{N}		Buch	5/3	10	Sand	2-24
								56	05/4	10	much	4-60
												Dib
										-		105
				_			-					
	EXTURE:	SOIL T		USIONS		IL REVIEW	SC		_			
	ZING FACTOR:				MATION: RATED SOIL:	DEPTH INFOR		ING WATER:	STAN		UITABLE TABLE SOIL	
											RBED SOIL	DISTU
	LOADING RATE:	LINEAR	EM:	1 OF SYST	AUM DEPTH O	MAXIA		CK;	BEDRO		ACTED SOIL	COWby
					REVIEW	SITE F						
	SETBACKS			LOT:	ENTS ON LOT	EASEN		LY	НАТ АРР	ALL TI	CHECK A	
		NE			UTILITY			ION			ND OR WETL	
			RIVER	ε	DRAINAGE	— п			IVER	M, RP	LAKE, STREA	
	POND, LAKE, STREAM, WETLAND				_	-	ION	EVATIO	AR FLOOD ELE	10 YE/		
		5.d	WELL		OTTIER	1 -			G DEPTH:			D WELL
			POND, L		IENTS ON LOT	EASEN		ION	VEGETAT IVER ION	AND W M, RP EVATIO	NND OR WETL LAKE, STREA OPLAIN AR FLOOD ELE LINE	POND, FLOOD 10 YEA BLUFF

OF MINN Client/ Ad				Legal D	escription/GPS:			Date:			
Lakeside Re	modelers		8475 Hidden Bay Trail N, Lake Elmo								
	t Material(s)		Outwash				N				
(circ	e all that app	NY CIL		Lacustrine /	Illuvium Loe	ss Organic	Matter B	drock			
Landscap (circ	e one)	Sumr		-		Slope . To	e Slope	Slope Shap	pe:		
Vegetation	woods		Soil Su	vey Map Unit	(S): 155C		Slope (%): 12%			
Weather d	anditions/Th	ne of Day	: Partly 61	loud. 10.	20		Elevation	/			
	onditional In	ac or Da			J = 410	Saturated 3					
Depth (in)	Texture		Matrix	Mottle	Redox	Indicator(s			I		
		Contie	Color(s)	Color(s)	Kind(s)	(see back)	Shape	Grade	Consistence		
0 /		Erne fi			Concentrations		Canada	Weak	-Loose-		
/	loam		1001 %.		Depletions		Blocky	Strong	Firm		
10			1 1		Gleyed -		Prismatic Sintie Grain	Loose	Extremely Firm		
							Massive		Rigid		
10/	Sand	<	. 07				Cinzeta-	Weak	Loose		
· /	loam	35	1041 /4		Concentrations		Blocky	Strong	Phable		
24	10g ha	35	11		Depletions Gleved		Printatic	Loose	Firm Extremely Firm		
-7					Gieyeu		Single Grain Mastive		Rigid		
24,	loamy	-	41			-	Gravalar	Weak	Coole -		
~7/	Sand	35	Der The		Concentrations	1	Platy Blocky	Moderate			
100		35	1.1.1	1.	Depletions		Priorgatio	Strong	Firm Extremely Firm		
. 30		1			Gleyed	· ·	Sector Ginto	Loose	Rigid		
~ /					-		Massive Generator	Weak	0.000		
50/	med		10 41		Concentrations		Platy	Moderate	TTANA		
6.			10yr 1/4	1	Depleticas	· ·	Blocky Prismatic	Strong	Firm		
12	Sand		. /		Gleyed		Siepe Gelter	Loose	Extremely Firm		
		+					Oranalar		Rigid		
		1.1		1 .	Concentrations		Platy	Wesk Moderate	Loose Friable		
				1	Depletions		Blocky	Strong	Finacie		
				1	Gleved		Printatic Signile Grain	Loose	Extremely Firm		
						1	Manive		Rigid		
							Craesdar Plate	Weak	Loose		
				1	Concentrations		Platy Blocky	Moderate	Friable		
				1 .	Depletions Gloved		Prismatic	Strong Locse	Firm Extensely Firm		
		1		1 1	oucyeu		Single Grain Manake		Rigid		

UNIVE OF MIN		. 1	Onsite Sewa	age Treat	ment Progr	am Soil I	Boring L	^{og} 82	· 🌺
Client/ A	ddress:		Legal Description/GPS: Date						la la
Lakeside R	emodelers			8475 Hidden	Bay Trail N, Lake	Elmo		3/	114
Soil Pare (cire	nt Material(s): cle all that app	(fill)	Outwash I	acustrine /	Illuvium Loe	s Organic	Matter B	edrock	
(cire	e Position: cle one)	Sum				Slope . To	e Slope	Slope Shap	e:
Vegetatio	on: woods conditions/Tim	ae of Da	Soil Sur r: Partly 210	vey Map Unit			Slope (%	~ ~70	
Depth (in)						Saturated S			
Depta (m)	Texture		Matrix Color(s)	Mottle Color(s)	Redox Kind(s)	Indicator(s (see back)) I Shape	Structure Grade	Consistence
0/4	loam	Coarse Erag 54	10417		Concentrations Depletions Glayed		Granular Platy Blocky Prismatic	Weak McGHIZE String Lone	Consistence Frate Firm Extremely Firm
					Gieyea	-	Single Grain Maggine		Rigid
8/28	toan F seed		104 34		Concentrations Depletions Gleyed		GrandsD Platy Blocky Pristnatic Single Grain	Weak Moderate Strong Loose	Doose Prinkle Firm Extremely Firm Rigid
28 39	loany fine send		10g, 1/g		Concentrations Depletions Gleyed		Massive Official Platy Blocky Primatic Single Grain Mataive	Weak Moderate Strong Losse	Loops Film Firm Extremely Firm Rigid
39	silt loam		104.46	39" 1045 41	Concentrations Depletions Gleyed		Orienther Paty Allector Primatic Single Grain Macture	Wenk Moderate Strong Loose	Losse Priable Extremely Firm Rigid
48 /54	loamy Fine Sand		10gr Hg	clear	Concentrations Depletions Glayed		Play Play Blacky Prisoatie Single Grain Mattive	Weak Medsiga Strong Loose	Loose Finite Finit Extremely Finite Rigid
					Concentrations Depletions Glayed		Orandar Flaty Blooky Primatic Single Grain Monion	Weak Moderate Strong Loose	Loose Friable Firm Extremely Firm Rizid

UNIVE OF MINI	NESOTA		Onsite Sewa	ige Treat	ment Progr	am Soil I	Boring Lo)g 13 3 3	- 🕰
Client/ Address:			Legal Description/GPS:					Date: 5/2/14	
Lakeside Remodelers		0	8475 Hidden Bay Trail N, Lake Elmo						917
(circ	nt Material(s): le all that app	5			lluvium Loe	ss Organic	Matter Be	drock	
(circ	e Position: de one)	Sum				t Slope . To		Slope Sha	pe:
Vegetatio	n: woods		Soil Surv	ey Map Unit		JG	Slope (%)	1296	
Weather e	conditions/Tin	ie of Da	Partly C	loudy 1	2:50 pm		Elevation		
Depth (in)	Texture		Matrix Color(s)	Mottle Color(s)	Redox Kind(s)	Saturated ! Indicator(s (see back)		Structure Grade	
0 .		Coarse Fran %	Calar(s)	Color(s)		(see back)	Granalia	Weak	Consistence
19	loam	Frag. St.	10gr 74		Concentrations Depletions Gleyed		Fizey Blocky Primmic Single Grain Mauring	Strong Loose	Finalie Firm Extremely Firm Rigid
9/28	loamy Fine Sand		1041 4/3		Concentrations Depletions Glayed		Oranatiz PERY Blocky Prismatic Single Omin Masthe	Weak Medicination Strong Loose	Firm Extranely Firm Rigid
28	lagun med Sán J		10yr 4/4		Concentrations Depletions Gleyed		Grazular Platy Biocky Prismatic Stager Gran	Weak Moderate Strong Locse	Loose Fills Fam Extranely Firm Rigid
					Concentrations Depletions Gleyed		Granular Platy Blocky Prignatic Single Grain Massive	Weak Moderate Strong Loose	Loose Frisble Firm Extremely Firm Rigid
					Concentrations Depletions Glayed		Greenber Platy Blocky Priematic Single Grain Massiwa	Weak Moderate Strong Loose	Loose Frishle Firm Extremely Firm Rigid
			eneby certify that I have co		Concentrations Depletions Glayed		Grassilar Platy Blocky Prismatic Single Grain Massive	Weak Moderate Strong Loose	Loose Frinkle Firm Extensity Firm Rigid

Brian L. Humpal, Inc. dba. Inspect Minnesota, Midwest Soil Testing

Relative to Subsurface Sewage Treatment System (SSTS) Compliance Inspections

- 1. This inspection/report is being performed for only the seller/owner of the property on which the SSTS is located. In such case that another party is paying for the inspection, the contract is between only said party and Brian L. Humpal, Inc.; there is no contract between Brian L. Humpal, Inc. and any other party unless otherwise noted.
- 3. Brian L. Humpal, Inc. has not been retained to warranty, guarantee, or certify the proper functioning of the SSTS for any period of time beyond the date of inspection or into the future. Because of the numerous factors (usage, maintenance, soil characteristics, previous failures, etc.) which may affect the proper operation of an SSTS, as well as the inability of Brian L. Humpal, Inc. to supervise or monitor the use or maintenance of the SSTS, the report shall not be construed as a warranty by Brian L. Humpal, Inc. that the SSTS will function properly for any particular party for any period of time.
- 4. Brian L. Humpal, Inc. is unable to verify the frequency and/or, quality of prior or future maintenance of the SSTS. Maintenance of the tank(s) must be performed through the tanks maintenance hole. The removal of solids from any location other than the maintenance hole is not a compliant method of maintenance. It is strongly recommended that maintenance covers be made accessible to the ground surface to facilitate proper maintenance.
- 5. Minimum Compliance Inspection requirements relative to this inspection and this report include <u>only</u> verification that the SSTS has tank(s) (septic tanks, lift tanks, dosing tanks, stilling tanks, etc.) which are watertight below the designed operating depth, the required separation between the bottom of the subsurface soil distribution medium and seasonally saturated soils, no back-ups of sewage into the dwelling, no discharge of sewage/effluent to the ground surface or surface waters, and no imminent safety hazards. Brian L. Humpal, Inc. does not inspect plumbing or pumps prior to the first SSTS component as these are plumbing components. The performance of exterior pumps and associated components are not inspected as they are considered to be maintenance items. Additionally, no indications relative to compliance with electrical code requirements have been made. It is recommended that any other applicable plumbing, electrical, housing, etc. inspections be performed by a qualified inspection business. Sewage back-up verification is limited to observing the floor drain area and/or the information supplied by the last occupants of the building prior to inspection. Brian L. Humpal, Inc. cannot guarantee that the information given to them by the last occupants of the building prior to inspection relative to back-ups is accurate.
- 4. Certification of this SSTS does not warranty future use beyond the date of the inspection. Any SSTS, old or new, can become hydraulically overloaded or discharge sewage/effluent to the ground surface as a result of more people moving into the house than were previously occupying the house, improper maintenance, heavy usage, leaking plumbing fixtures, groundwater infiltration, tree roots, freezing conditions, surface drainage problems, poor initial design, poor construction practices, or unsuitable materials used in constructing the system; the system can also simply stop working because of its age. An SSTS that has been properly designed and installed, properly maintained, and used in the manner for which the system was designed can be expected to provide service for twenty to twenty-five years on average. Some parts of the SSTS such as alarms, switches, pumps, filters, etc. will most likely have to be repaired or replaced over the lifetime of the system.
- 5. A Compliance Inspection is not meant to be a test or inspection for longevity of the system; a Compliance Inspection is strictly for the purpose of determining if the SSTS is protective of public health and safety, as well as the groundwater at the date and time the inspection was performed. This inspection is not intended to determine if the SSTS was originally designed or installed to past or present MPCA or other Local Government Unit code requirements. This inspection is not intended to determine if the SSTS was designed and/or installed to support the anticipated flow from the building as the use of the building may have changed since the design and construction of the SSTS due to the addition of bedrooms, occupants, etc. In addition, this inspection is not intended to determine the quality of the original SSTS design, the quality of the construction practices used while installing the SSTS, or the quality of the materials used in constructing the SSTS.
- 6. Brian L. Humpal, Inc. cannot guarantee the performance of SSTS products/components such as: gravelless pipe, chamber trenches, effluent filters, tanks, sewage pre-treatment components, piping, etc. Products such as gravelless pipe are no longer approved for installation in the State of Minnesota and may have a significantly reduced performance and/or life expectancy.
- 7. WINTER WORK: By accepting this report, it is understood that inspections conducted during winter months (approximately November 1st through April 1st) are more difficult to perform because of possible snow cover and/or ground frost. SSTS components such as tanks, maintenance covers, tank inspection pipes, subsurface distribution medium inspection pipes, and soil treatment areas are more difficult or impossible to locate due to snow cover and/or ground frost. In addition, soil borings are more difficult to perform due to snow cover and/or ground frost. Brian L. Humpal, Inc. will attempt to use the same level of standards when performing work during winter periods as when performing work during non-winter periods. However, the recipient of this report understands that because of the aforementioned considerations, the same level of standards may not be possible.
- 8. By accepting this report, the client understands that Brian L. Humpal, Inc. will not be responsible for any monetary damages exceeding the fee for the services provided.

Subsurface Sewage[®]Treatment Systems Non-transferable Business License

Inspect Minnesota, Midwest Soil Testing

License Expires: 12/22/2019

Issued: 11/20/2018

Specialty Area(s):

License # L2896

Installer Maintainer Service Provider Advanced Designer Advanced Inspector

Designated Certified Individual(s):

Cert #	Name	Certification Expires:
C9633	Anthony P Scully	3/5/2020
•	Installer, Designer (Apprentice)	
C5342	Brian L Humpal	10/15/2023
	Installer, Maintainer, Serv Prov, Adv De	esigner, Adv Inspector
C9852	Christopher R Uebe	3/4/2021
	Designer, Inspector	

MINNESOTA POLLUTION CONTROL AGENCY

520 Lafayette Road North St. Paul, Minnesota 55155-4194

Nich Haig

Nick Haig, Supervisor Certification and Training Unit
